
SINGLE STOREY HOUSE PROJECT PRIMAVERA P6

A project done by Joshua Jerson Naveen


GANT CHART

Activity ID	Activity Name	Planned Duration	Start	Finish	Predeces	Successo	Planned Labor Units	Planned Total Cost
Project: V-1000 Residential Villa Pro		60	25-A	18-Jul-24			2660	₹907,120.00
WBS: V-1000.0 Priliminary Works		5	25-A	01-May-			0	₹20,000.00
A1000	Project Start	0	25-A			A1010	0	₹0.00
A1010	Initial Prepatory Works	5	25-A	01-May-	A1000	A1020	0	₹20,000.00
WBS: V-1000.1 Sub Structural Works		5	02-M	08-May-			616	₹123,280.00
A1020	Excavation	1	02-M	02-May-	A1010	A1030	160	₹29,200.00
A1030	Foundation Masonary	4	03-M	08-May-	A1020	A1040	456	₹94,080.00
WBS: V-1000.2 Super structional Wor		49	09-M	17-Jul-24			2036	₹754,240.00
WBS: V-1000.2.1 Structural Works		20	09-M	05-Jun-			772	₹447,560.00
A1040	Pinth Beam	1	09-M	09-May-	A1030	A1050	72	₹17,160.00
A1050	Block Work Masonary in Super Structure	7	10-M	20-May-	A1040	A1060	268	₹85,840.00
A1060	Coloum Steel Work	1	21-M	21-May-	A1050	A1070	24	₹8,120.00
A1070	Coloumn Form Work	1	21-M	21-May-	A1060	A1080	24	₹24,320.00
A1080	Coloumn Concrete Work	1	22-M	22-May-	A1070	A1090	56	₹66,520.00
A1090	Slab And Beam form Work	6	23-M	30-May-	A1080	A1100	144	₹145,920.00
A1100	Slab and Beam Steel Work	3	31-M	04-Jun-	A1090	A1110	72	₹24,360.00
A1110	Slab and Beam Concrete Work	1	05-J	05-Jun-	A1100	A1120	112	₹75,320.00
WBS: V-1000.2.2 Architechtural works		14	27-J	17-Jul-24			1264	₹306,680.00
A1120	Plaster Work	8	27-J	08-Jul-24	A1110	A1130	864	₹181,760.00
A1130	Flooring Work	1	09-J	09-Jul-24	A1120	A1140	112	₹21,720.00
A1140	Window and Door Installation	1	10-J	10-Jul-24	A1130	A1150	80	₹20,000.00
A1150	Paint Work	4	11-Ju	17-Jul-24	A1140	A1160	208	₹83,200.00
WBS: V-1000.3 Final Commisioning W		1	17-J	18-Jul-24			8	₹9,600.00
A1160	Final Check List	1	17-J	18-Jul-24	A1150	A1170	8	₹9,600.00
WBS: V-1000.4 Project close out		0	18-J	18-Jul-24			0	₹0.00
A1170	Project Handover	0		18-Jul-24	A1160		0	₹0.00

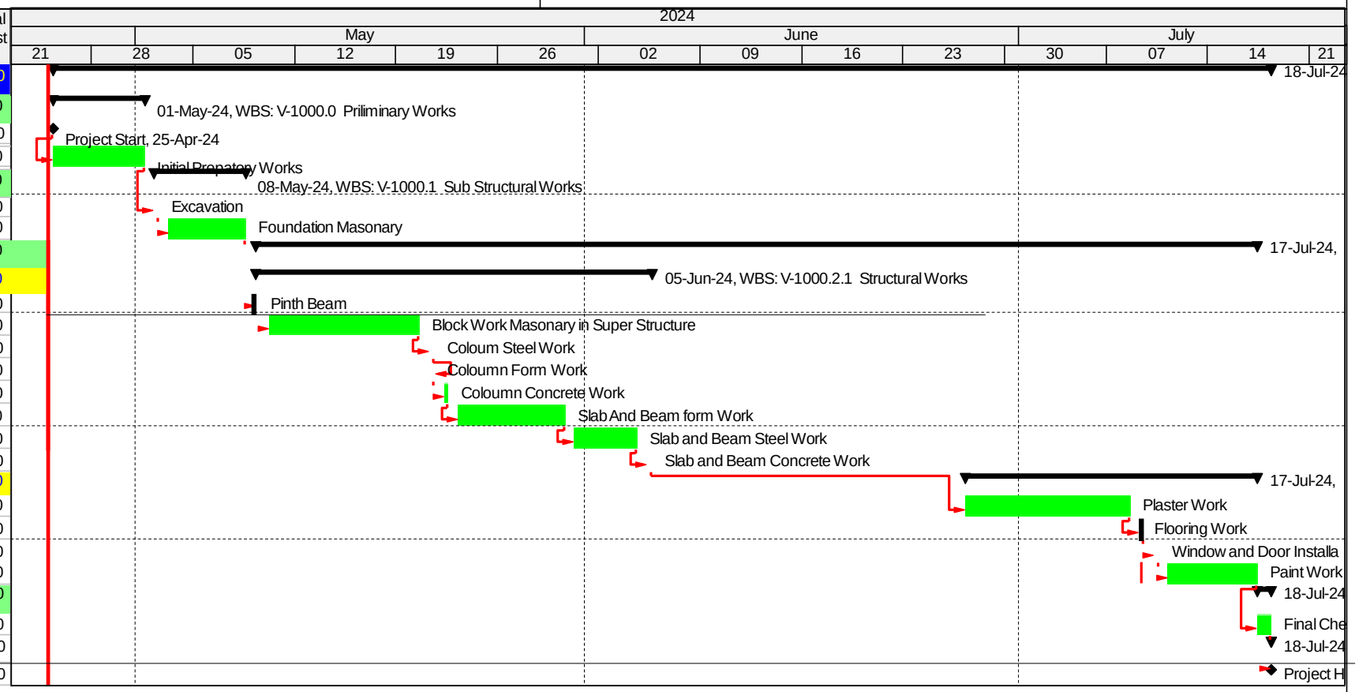

© Oracle Corporation

ACTIVITY USAGE PROFILE

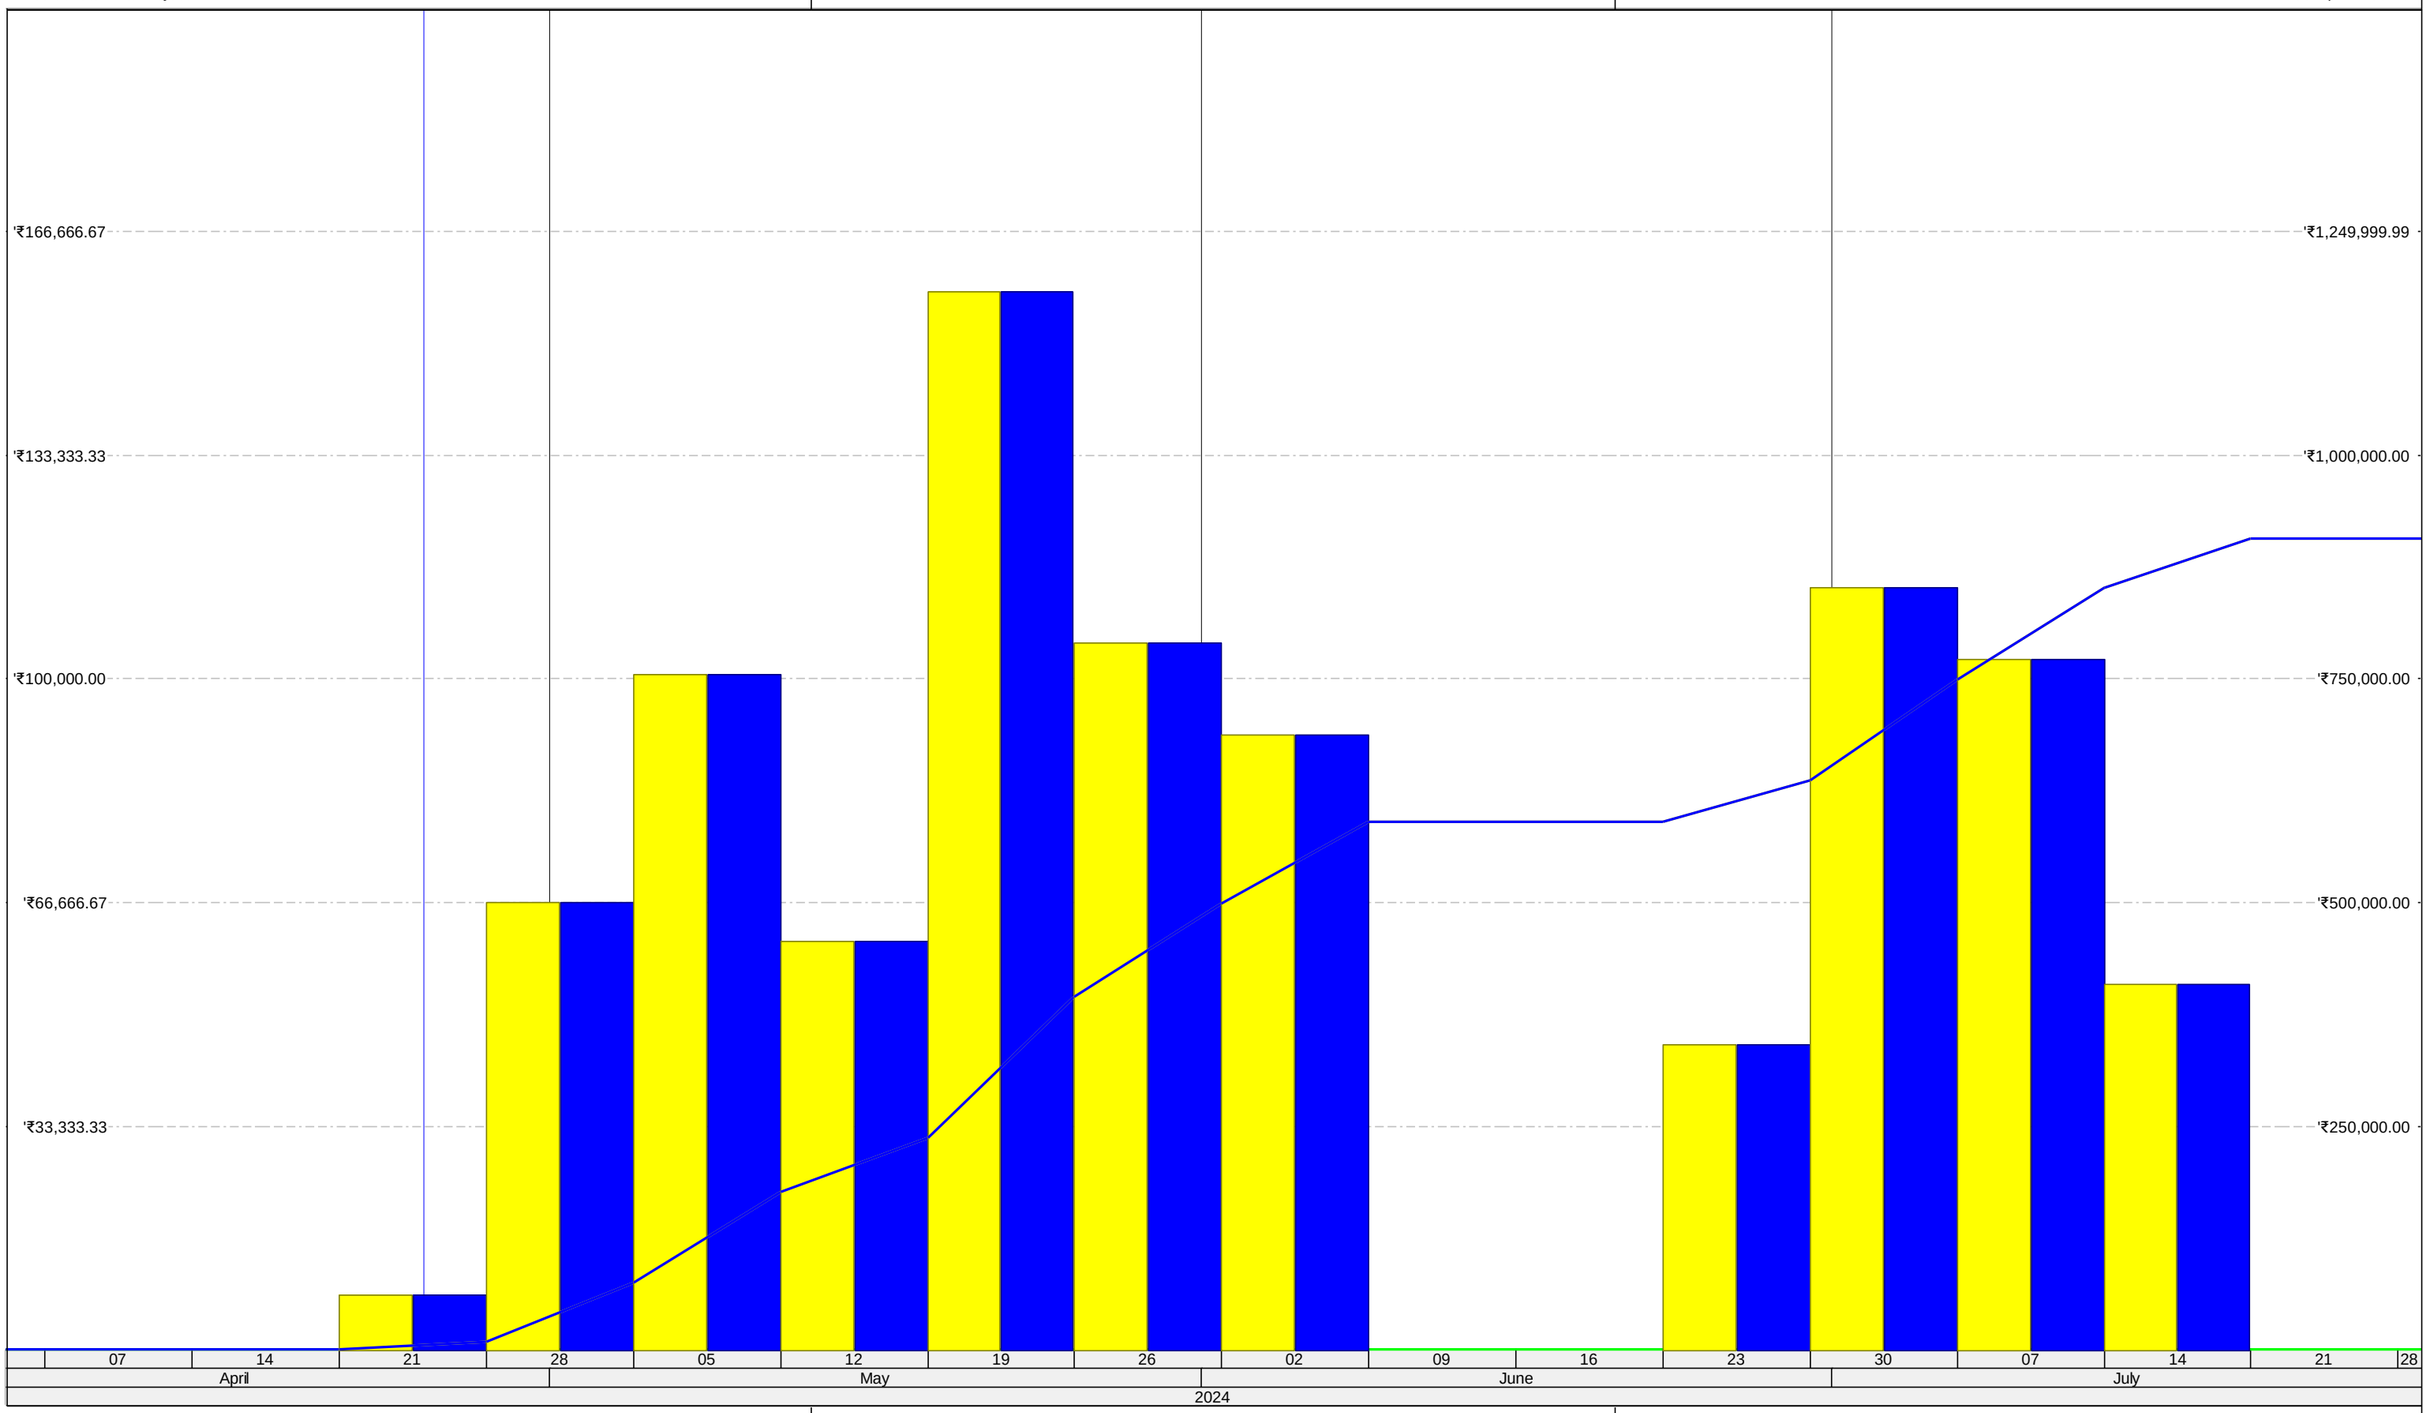

Cost

Budgeted Total Actual Total Remaining Total

TASK filter: All Activities

© Oracle Corporation

RESOURSE USAGE SPREADSHEET

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

Activity ID	Start	Finish	Remaining Units
Stee	21-May-24	04-Jun-24	
A1060	21-May-24	21-May-24	
A1100	31-May-24	04-Jun-24	

| 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

Activity ID	Start	Finish	Remaining Units
Pain	11-Jul-24	17-Jul-24	
A1150	11-Jul-24	17-Jul-24	

2024

April					May					June					July				August				September				October				November				December		
24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15
															96	112																					
															96	112																					


© Oracle Corporation

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

Activity ID	Start	Finish	Remaining Units
Paint	11-Jul-24	17-Jul-24	
A1150	11-Jul-24	17-Jul-24	



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

Activity ID	Start	Finish	Remaining Units
Steel	09-May-24	04-Jun-24	
A1060	21-May-24	21-May-24	
A1040	09-May-24	09-May-24	
A1100	31-May-24	04-Jun-24	


| 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

| Activity ID | Start | Finish | Remaining Units | 2024 | | |

Activity ID	Start	Finish	Remaining Units
Exc	02-May-24	02-May-24	
A1020	02-May-24	02-May-24	



TASK filter: All Activities


© Oracle Corporation

RESOURSE USAGE PROFILE

Residential Villa Project

Mason

30-Apr-24 05:32

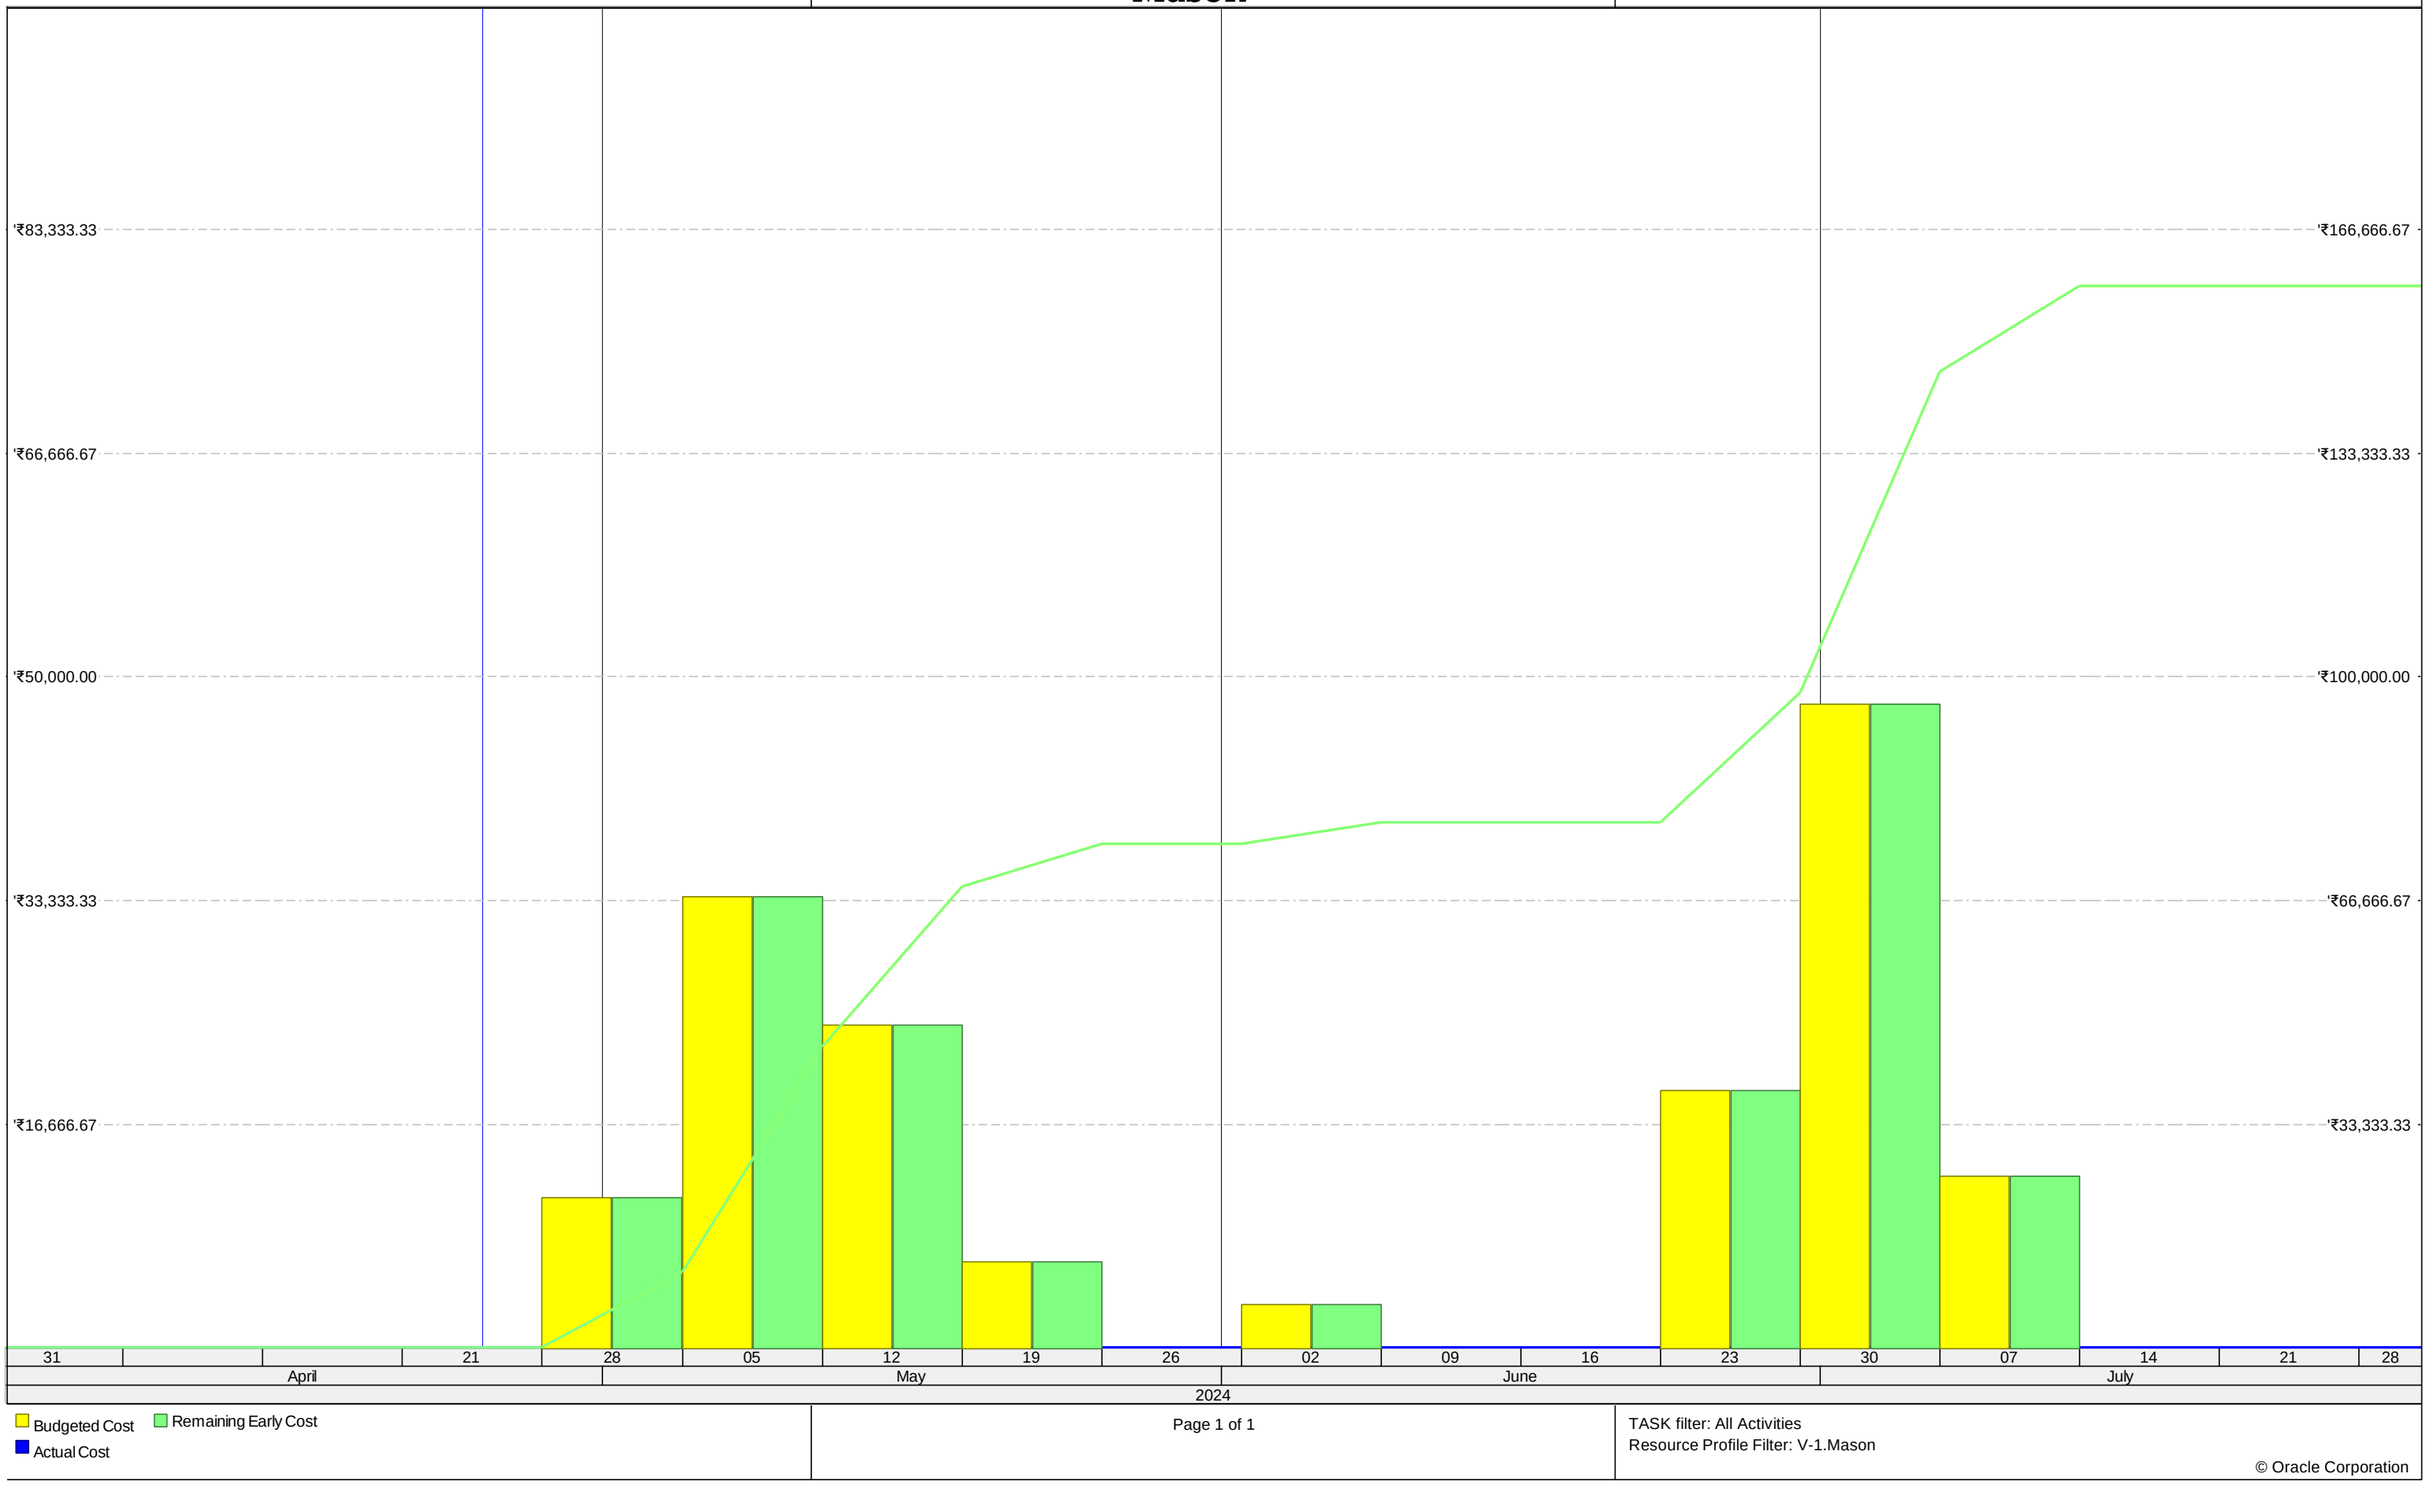

Page 1 of 1


TASK filter: All Activities
Resource Profile Filter: V-1.Mason

© Oracle Corporation

Residential Villa Project

Labourer

30-Apr-24 05:33

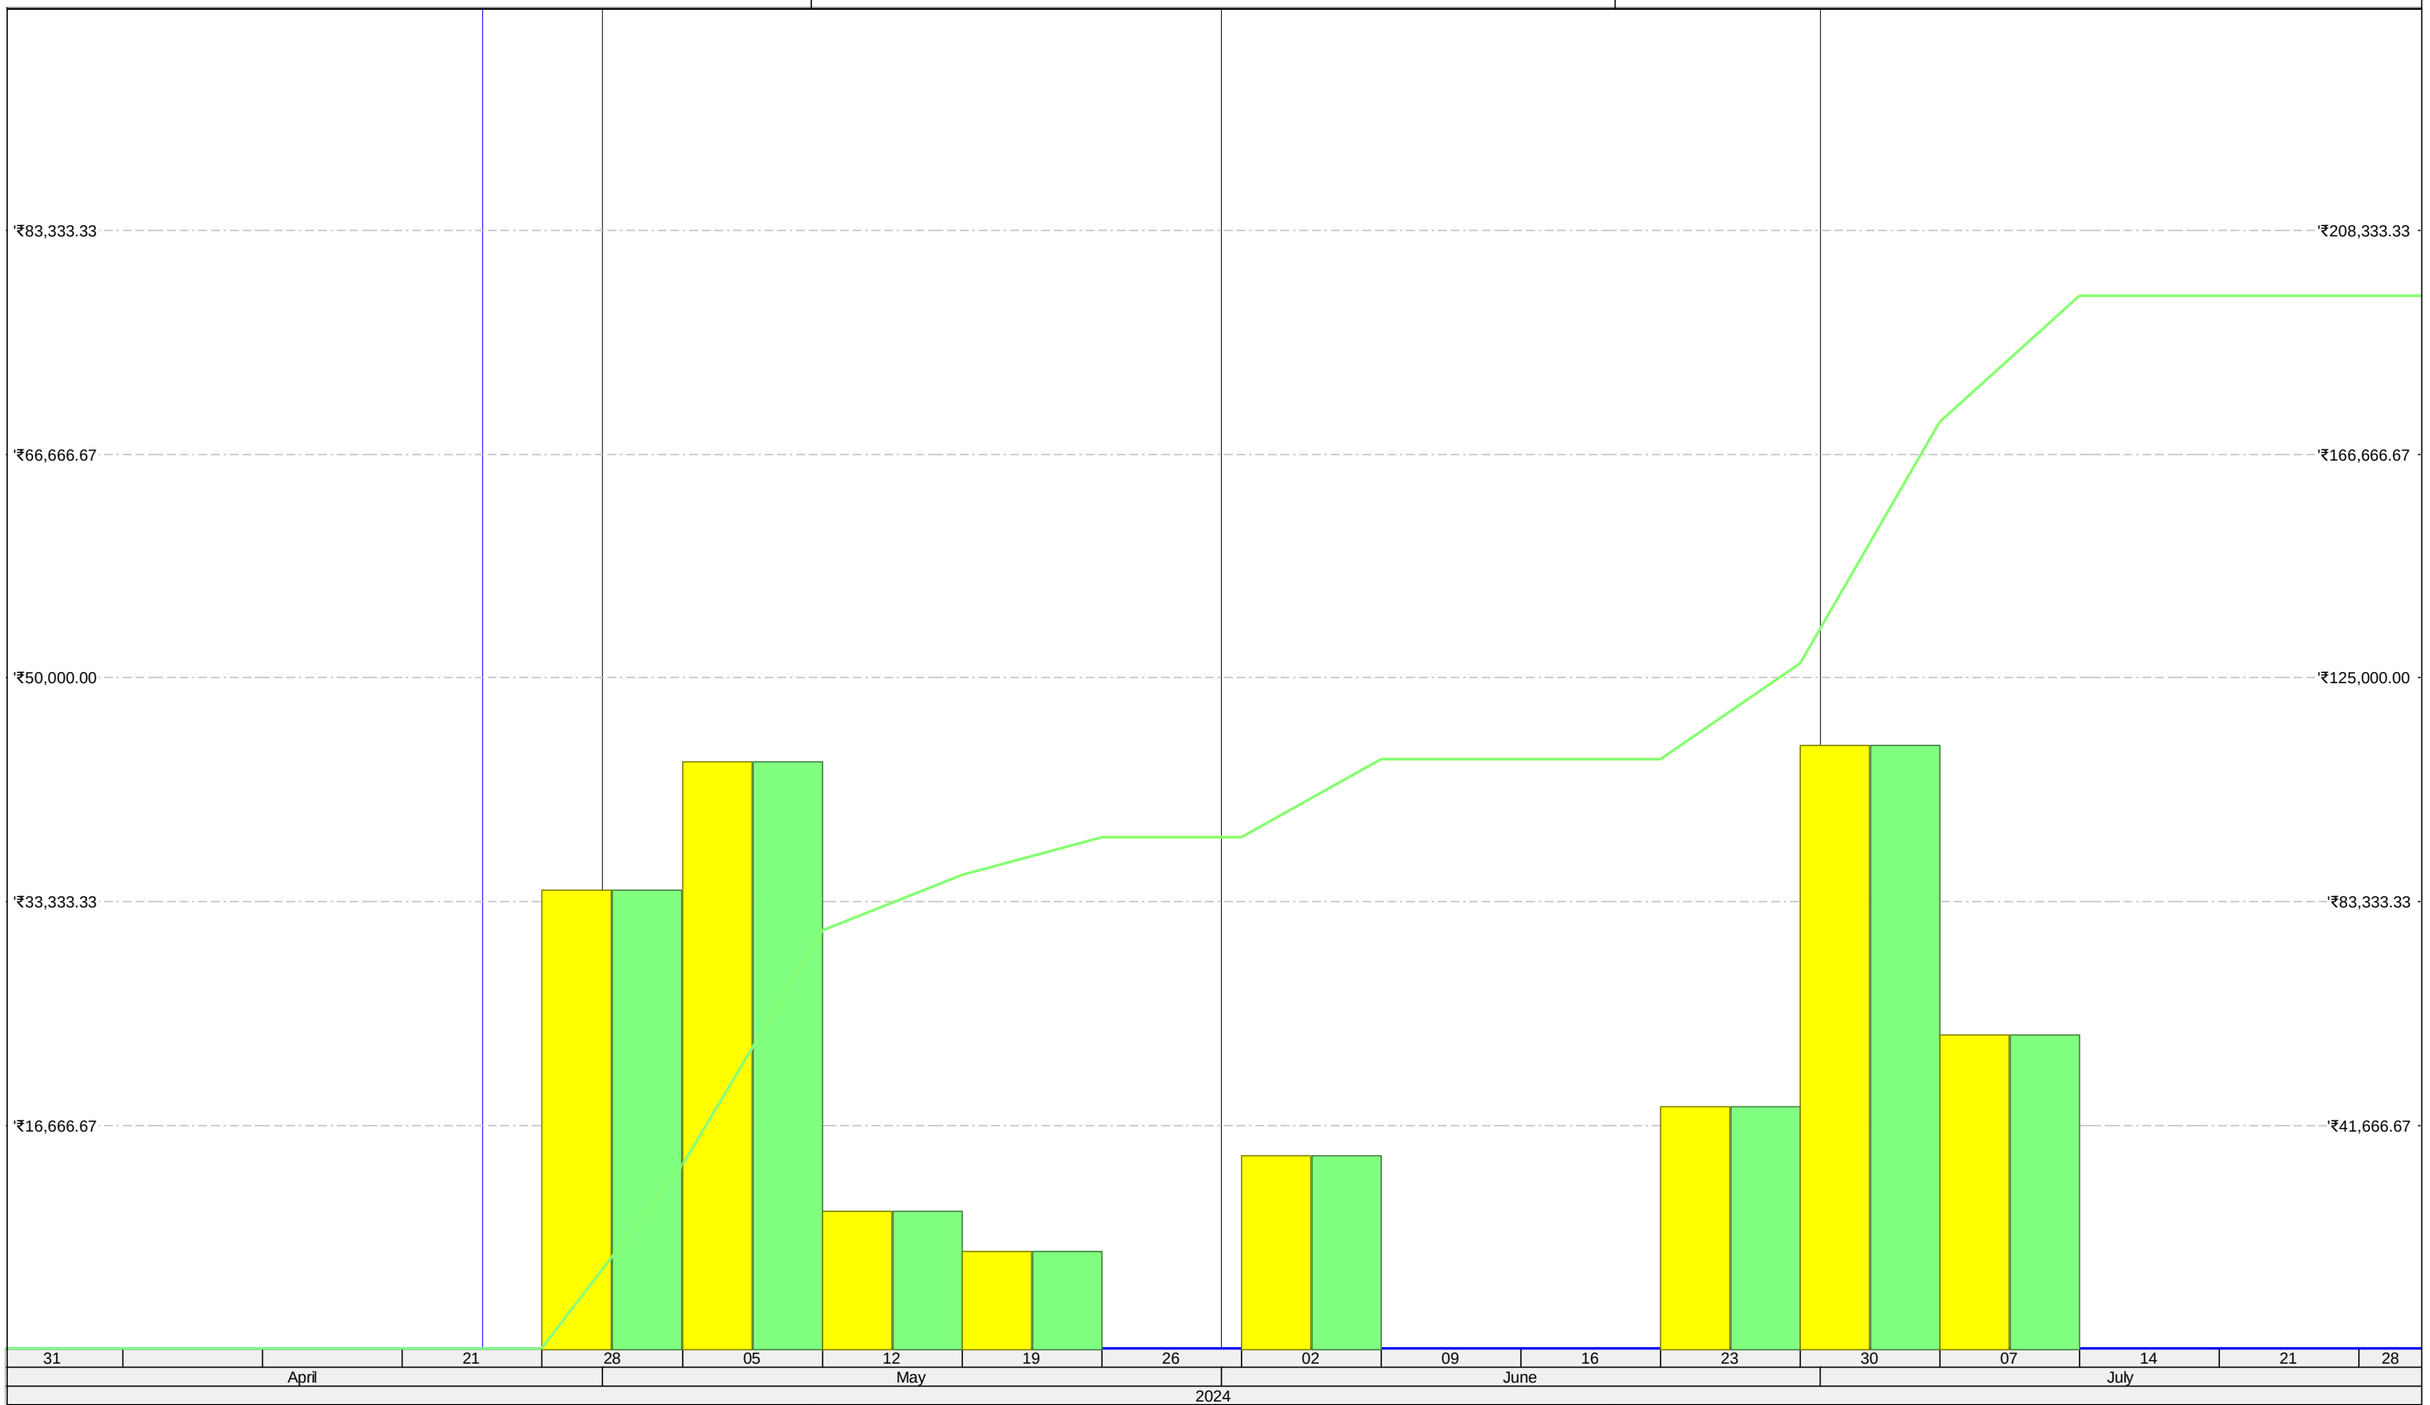

Page 1 of 1


TASK filter: All Activities
Resource Profile Filter: V-2.Labourer

© Oracle Corporation

Carpenter

Residential Villa Project

30-Apr-24 05:33

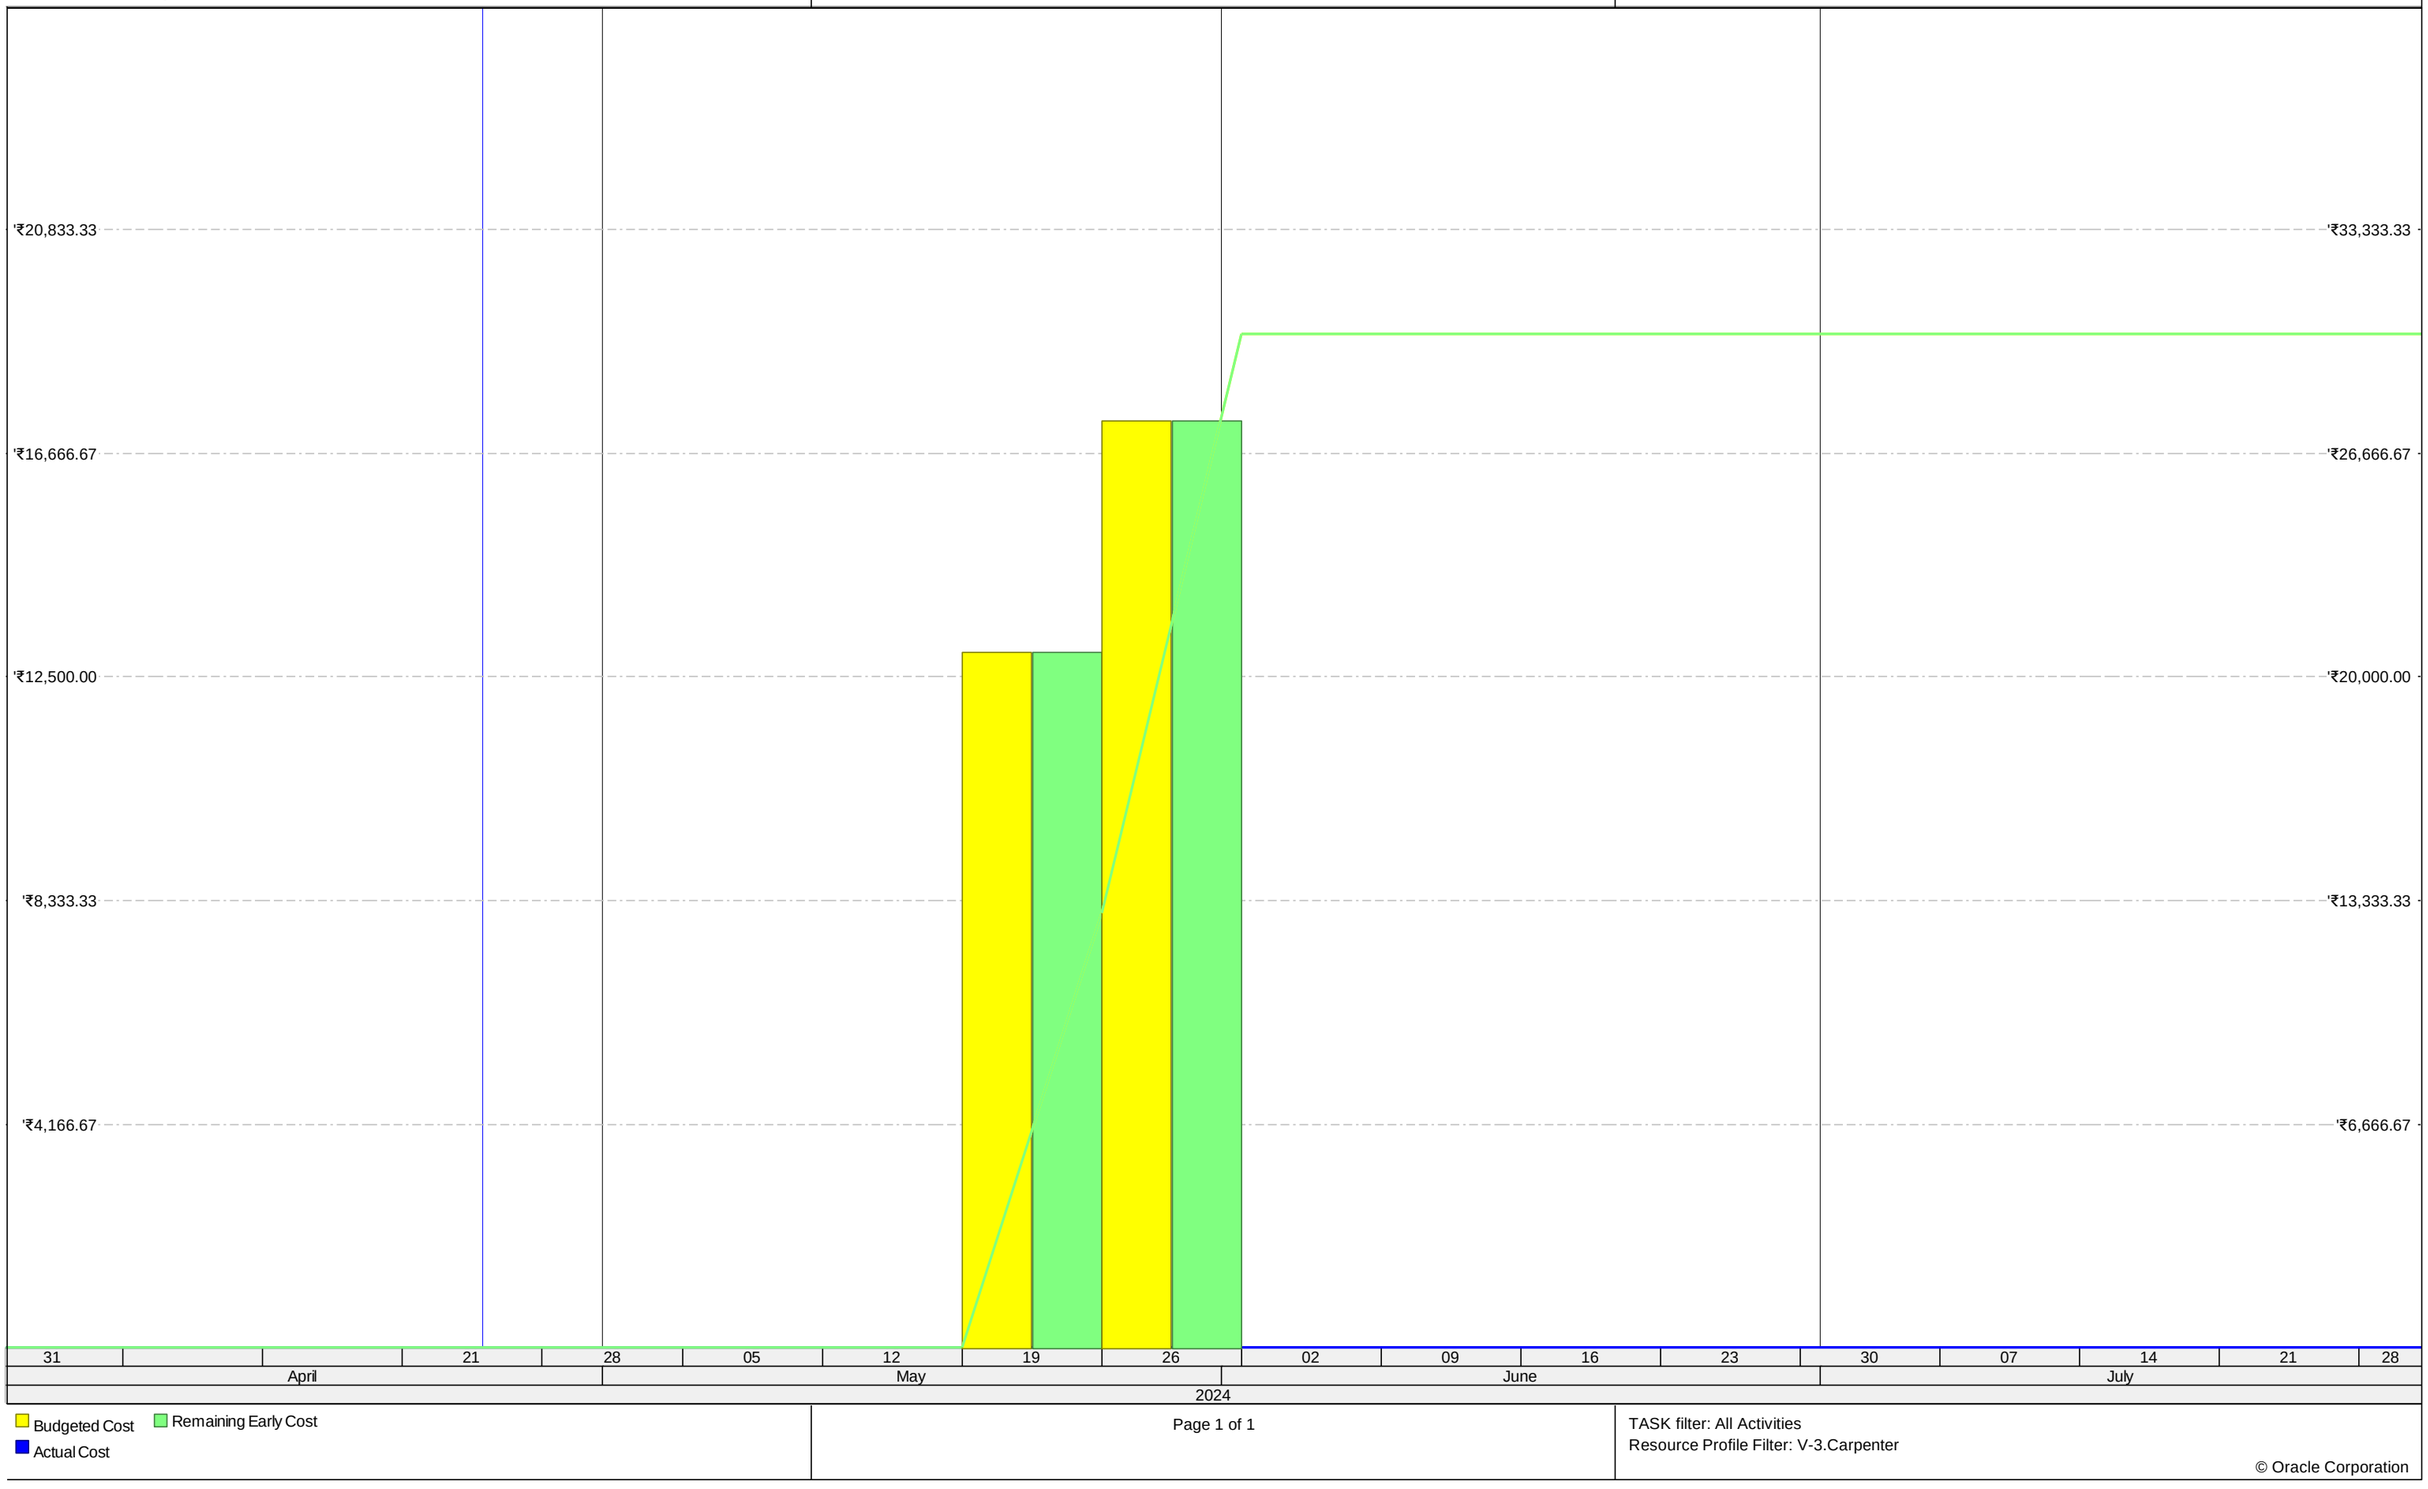

Budgeted Cost
Remaining Early Cost
Actual Cost


TASK filter: All Activities
Resource Profile Filter: V-3.Carpenter

© Oracle Corporation

Residential Villa Project

Welder

30-Apr-24 05:34

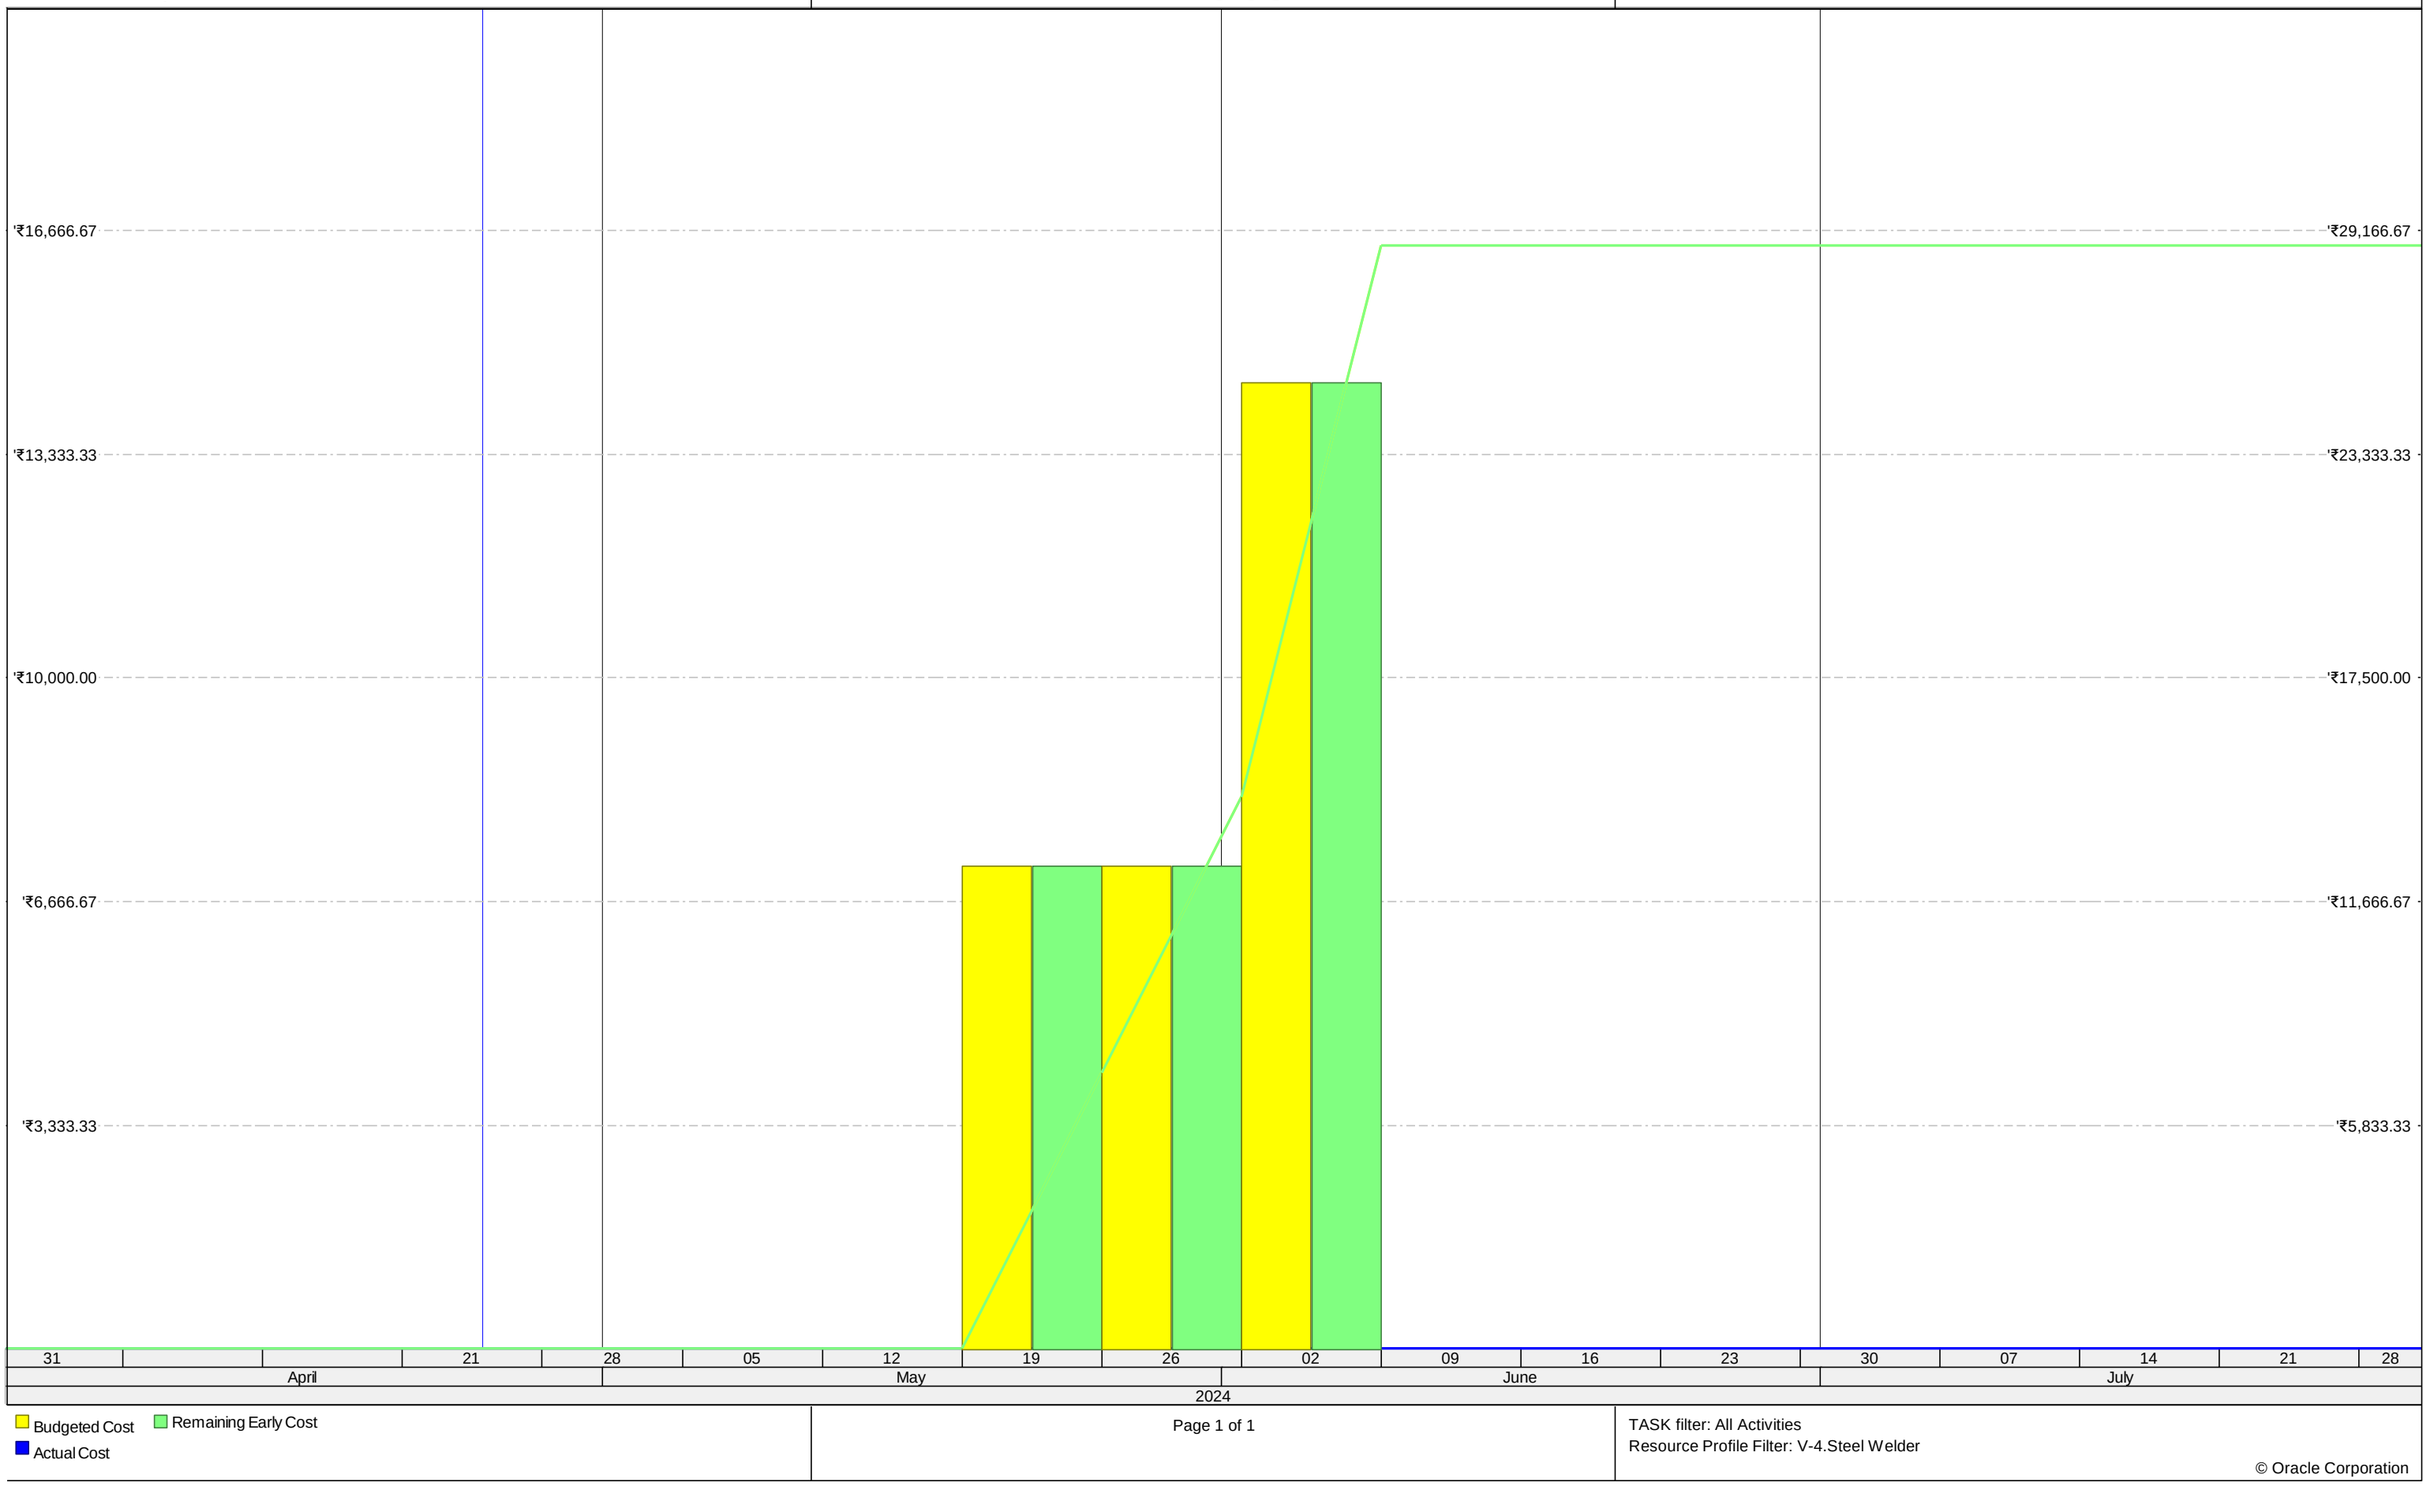

Budgeted Cost
Remaining Early Cost
Actual Cost

Page 1 of 1


TASK filter: All Activities
Resource Profile Filter: V-4.Steel Welder

© Oracle Corporation

Wood Worker

Residential Villa Project

30-Apr-24 05:34

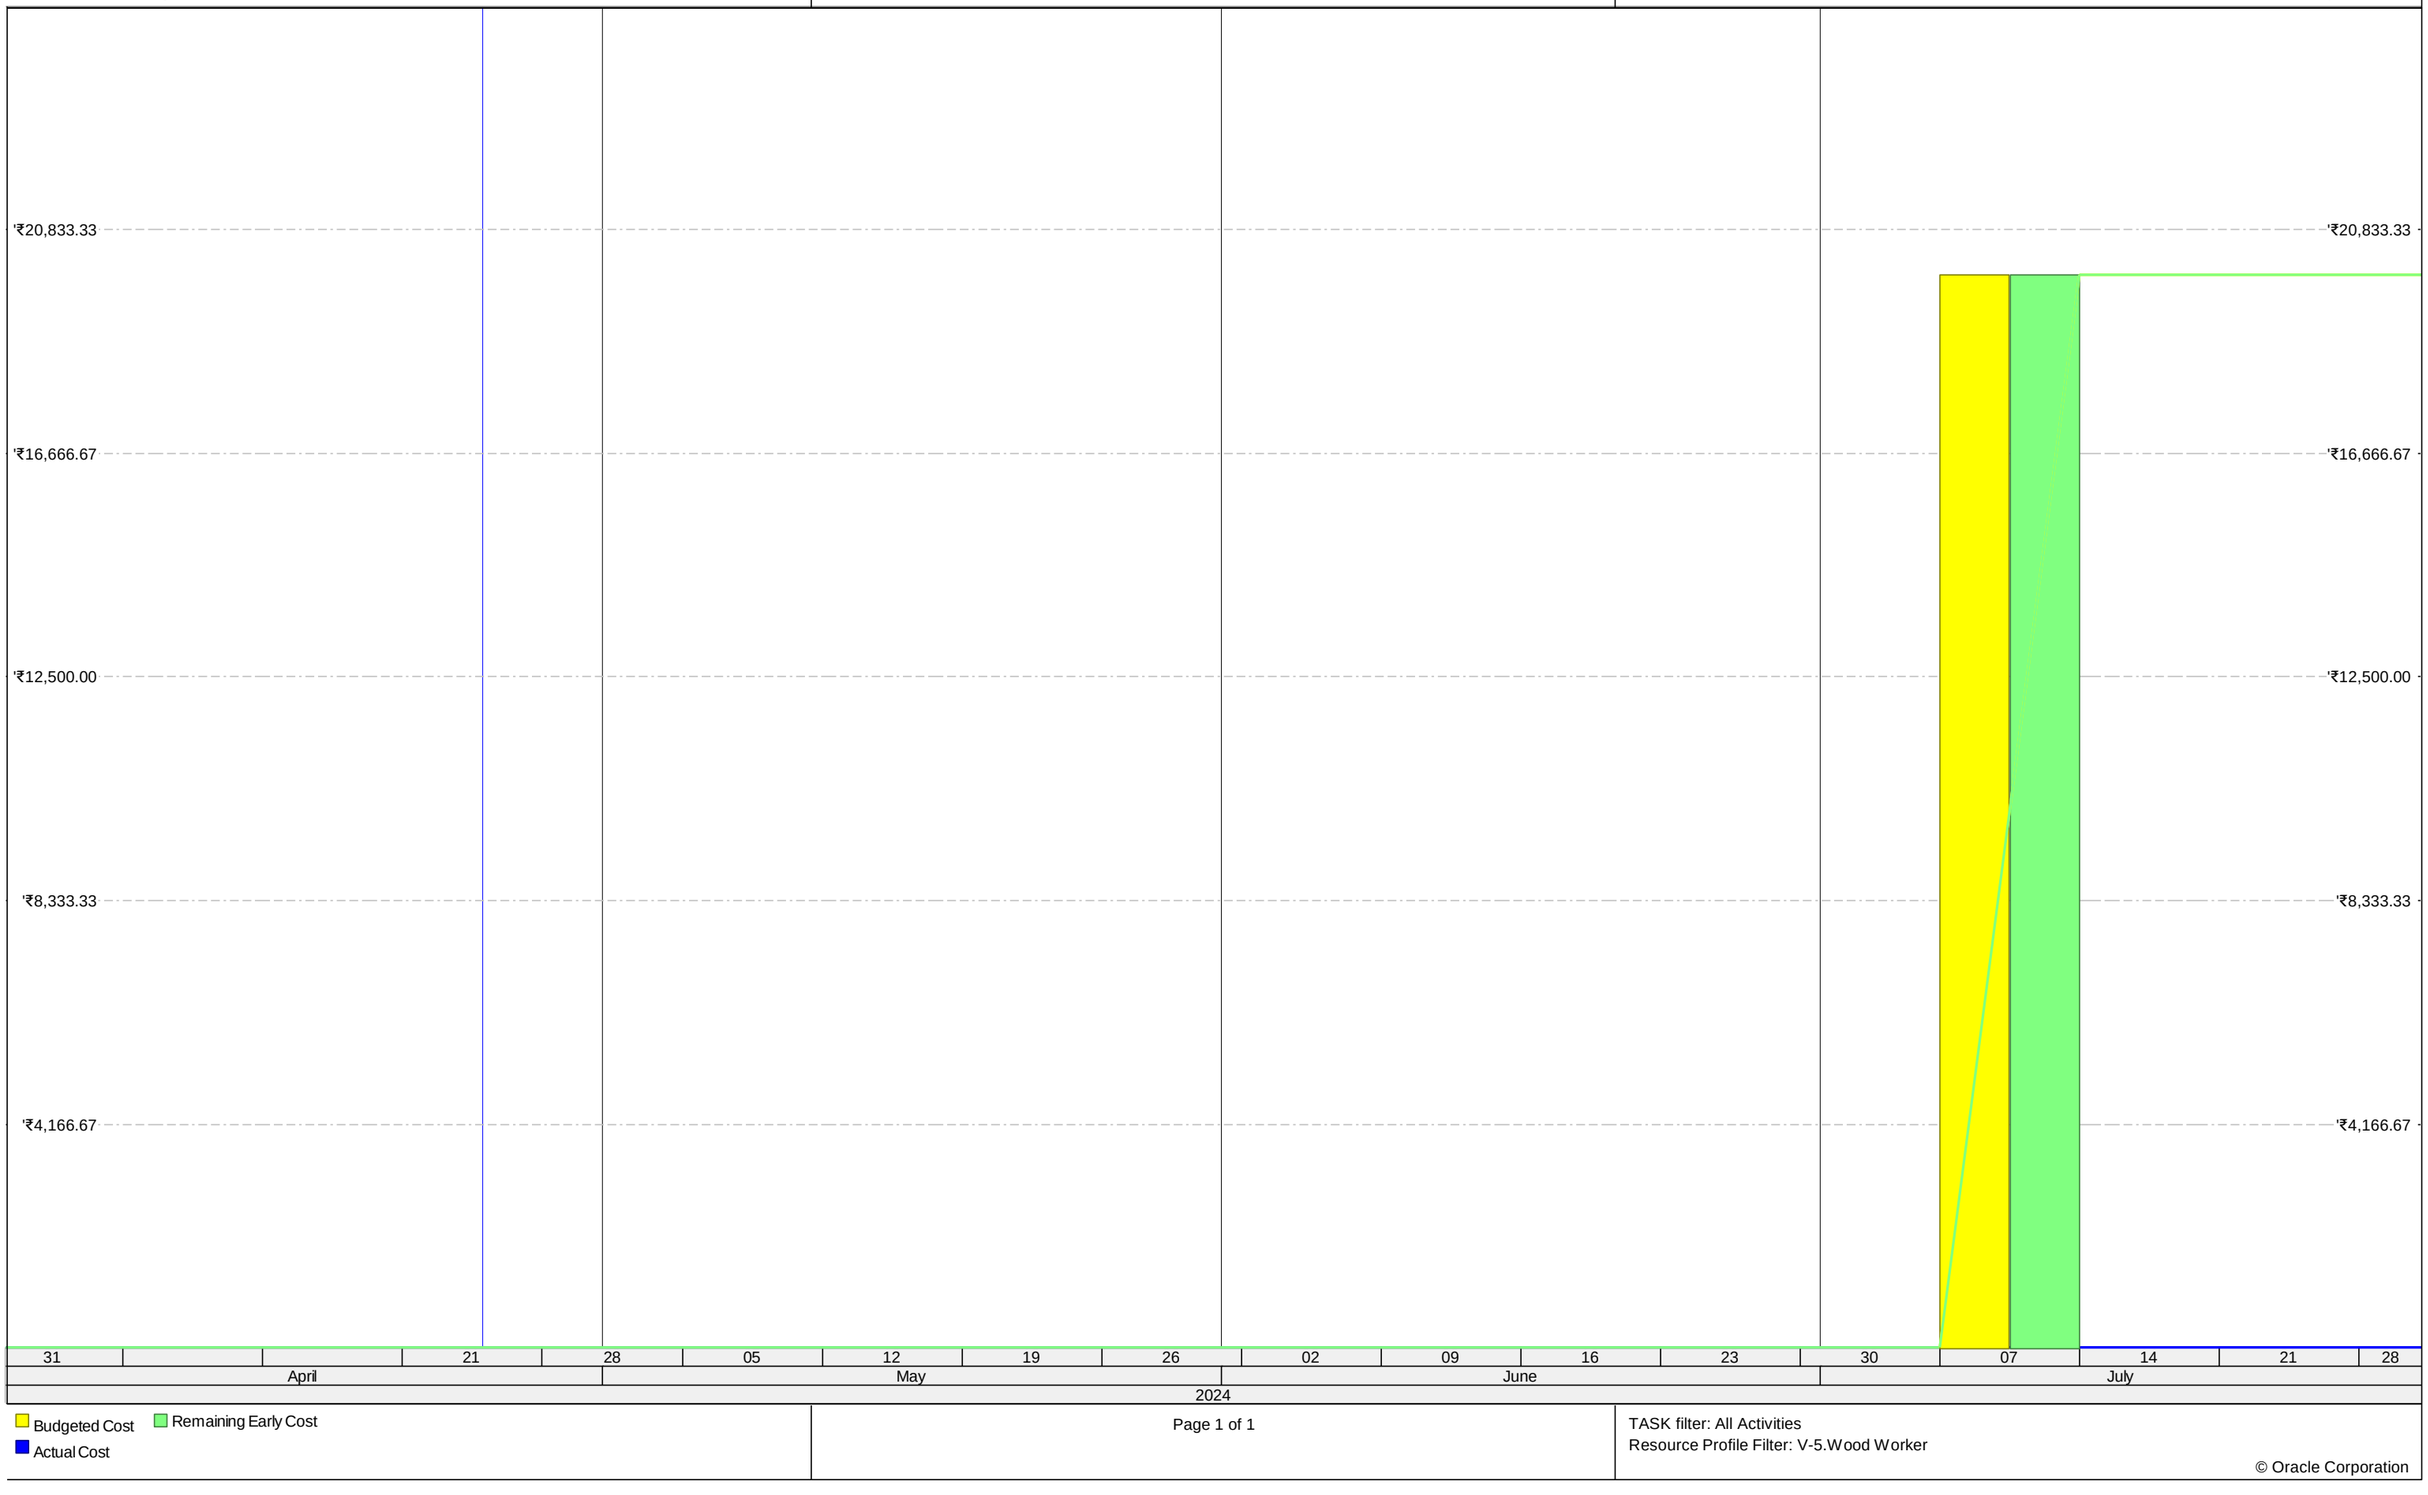

Budgeted Cost
Remaining Early Cost
Actual Cost

TASK filter: All Activities
Resource Profile Filter: V-5.Wood Worker

© Oracle Corporation


07

14

Painter

Residential Villa Project

30-Apr-24 05:34

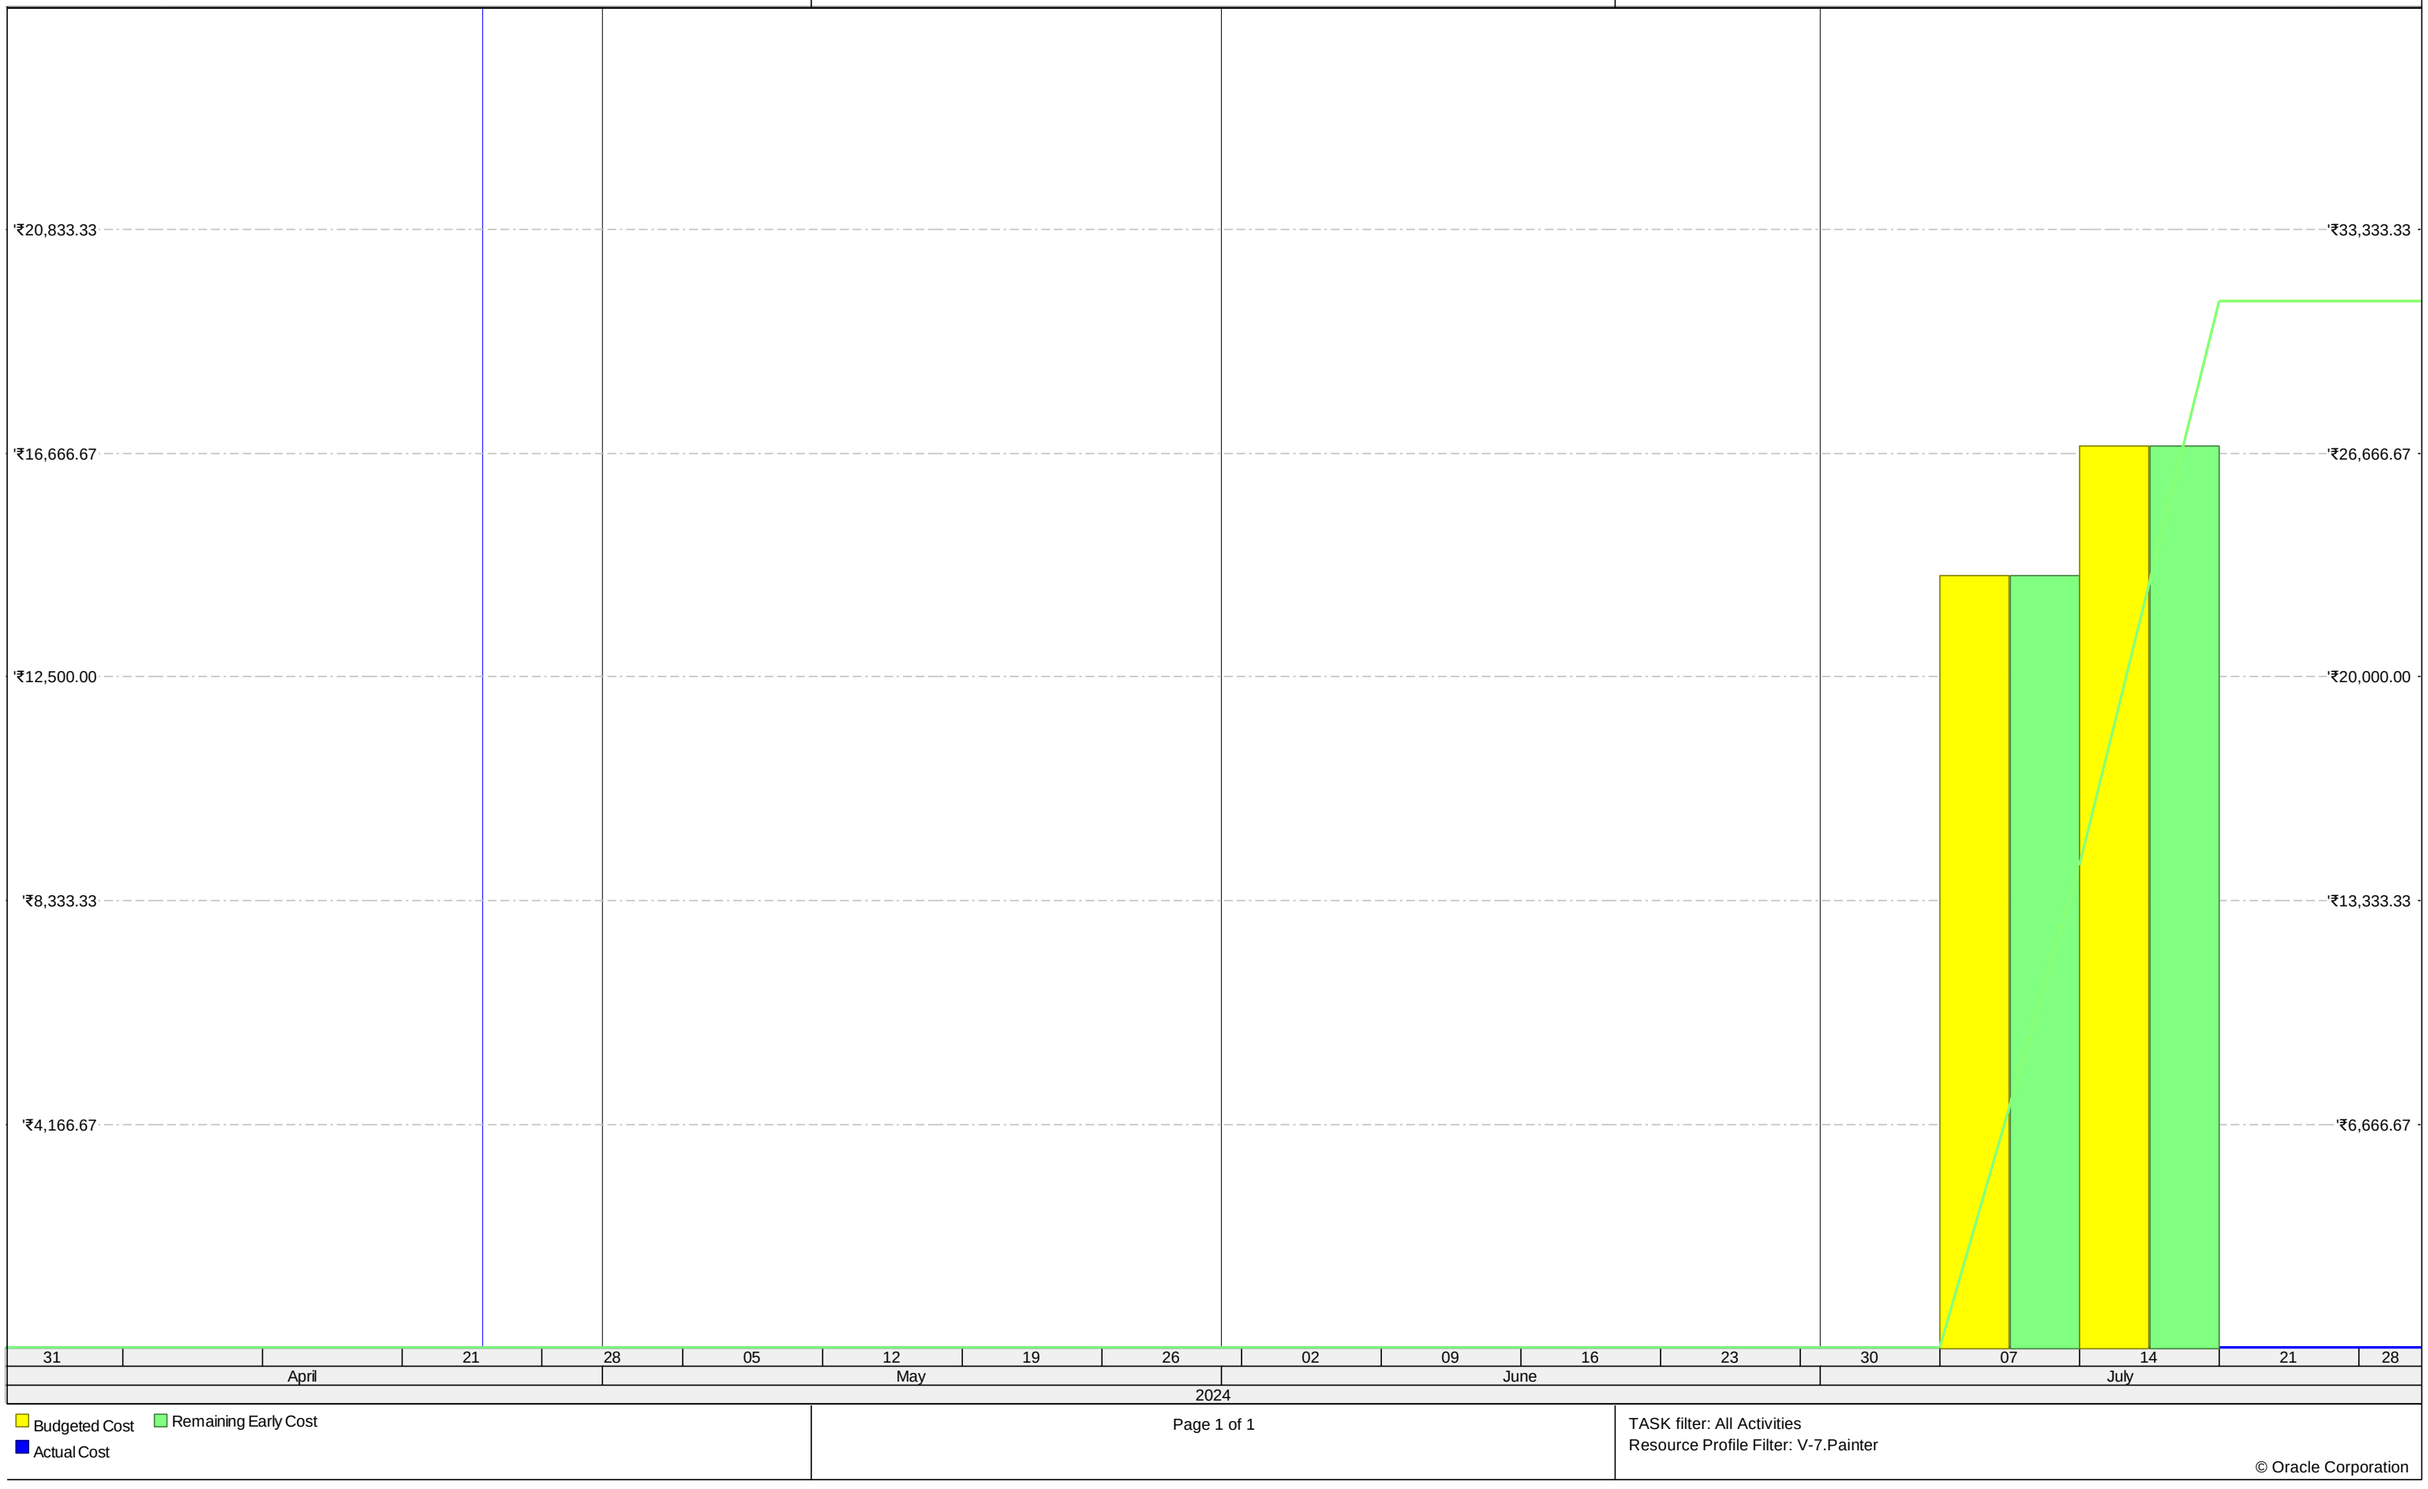


Budgeted Cost
Remaining Early Cost
Actual Cost

TASK filter: All Activities
Resource Profile Filter: V-7.Painter

© Oracle Corporation

07

14

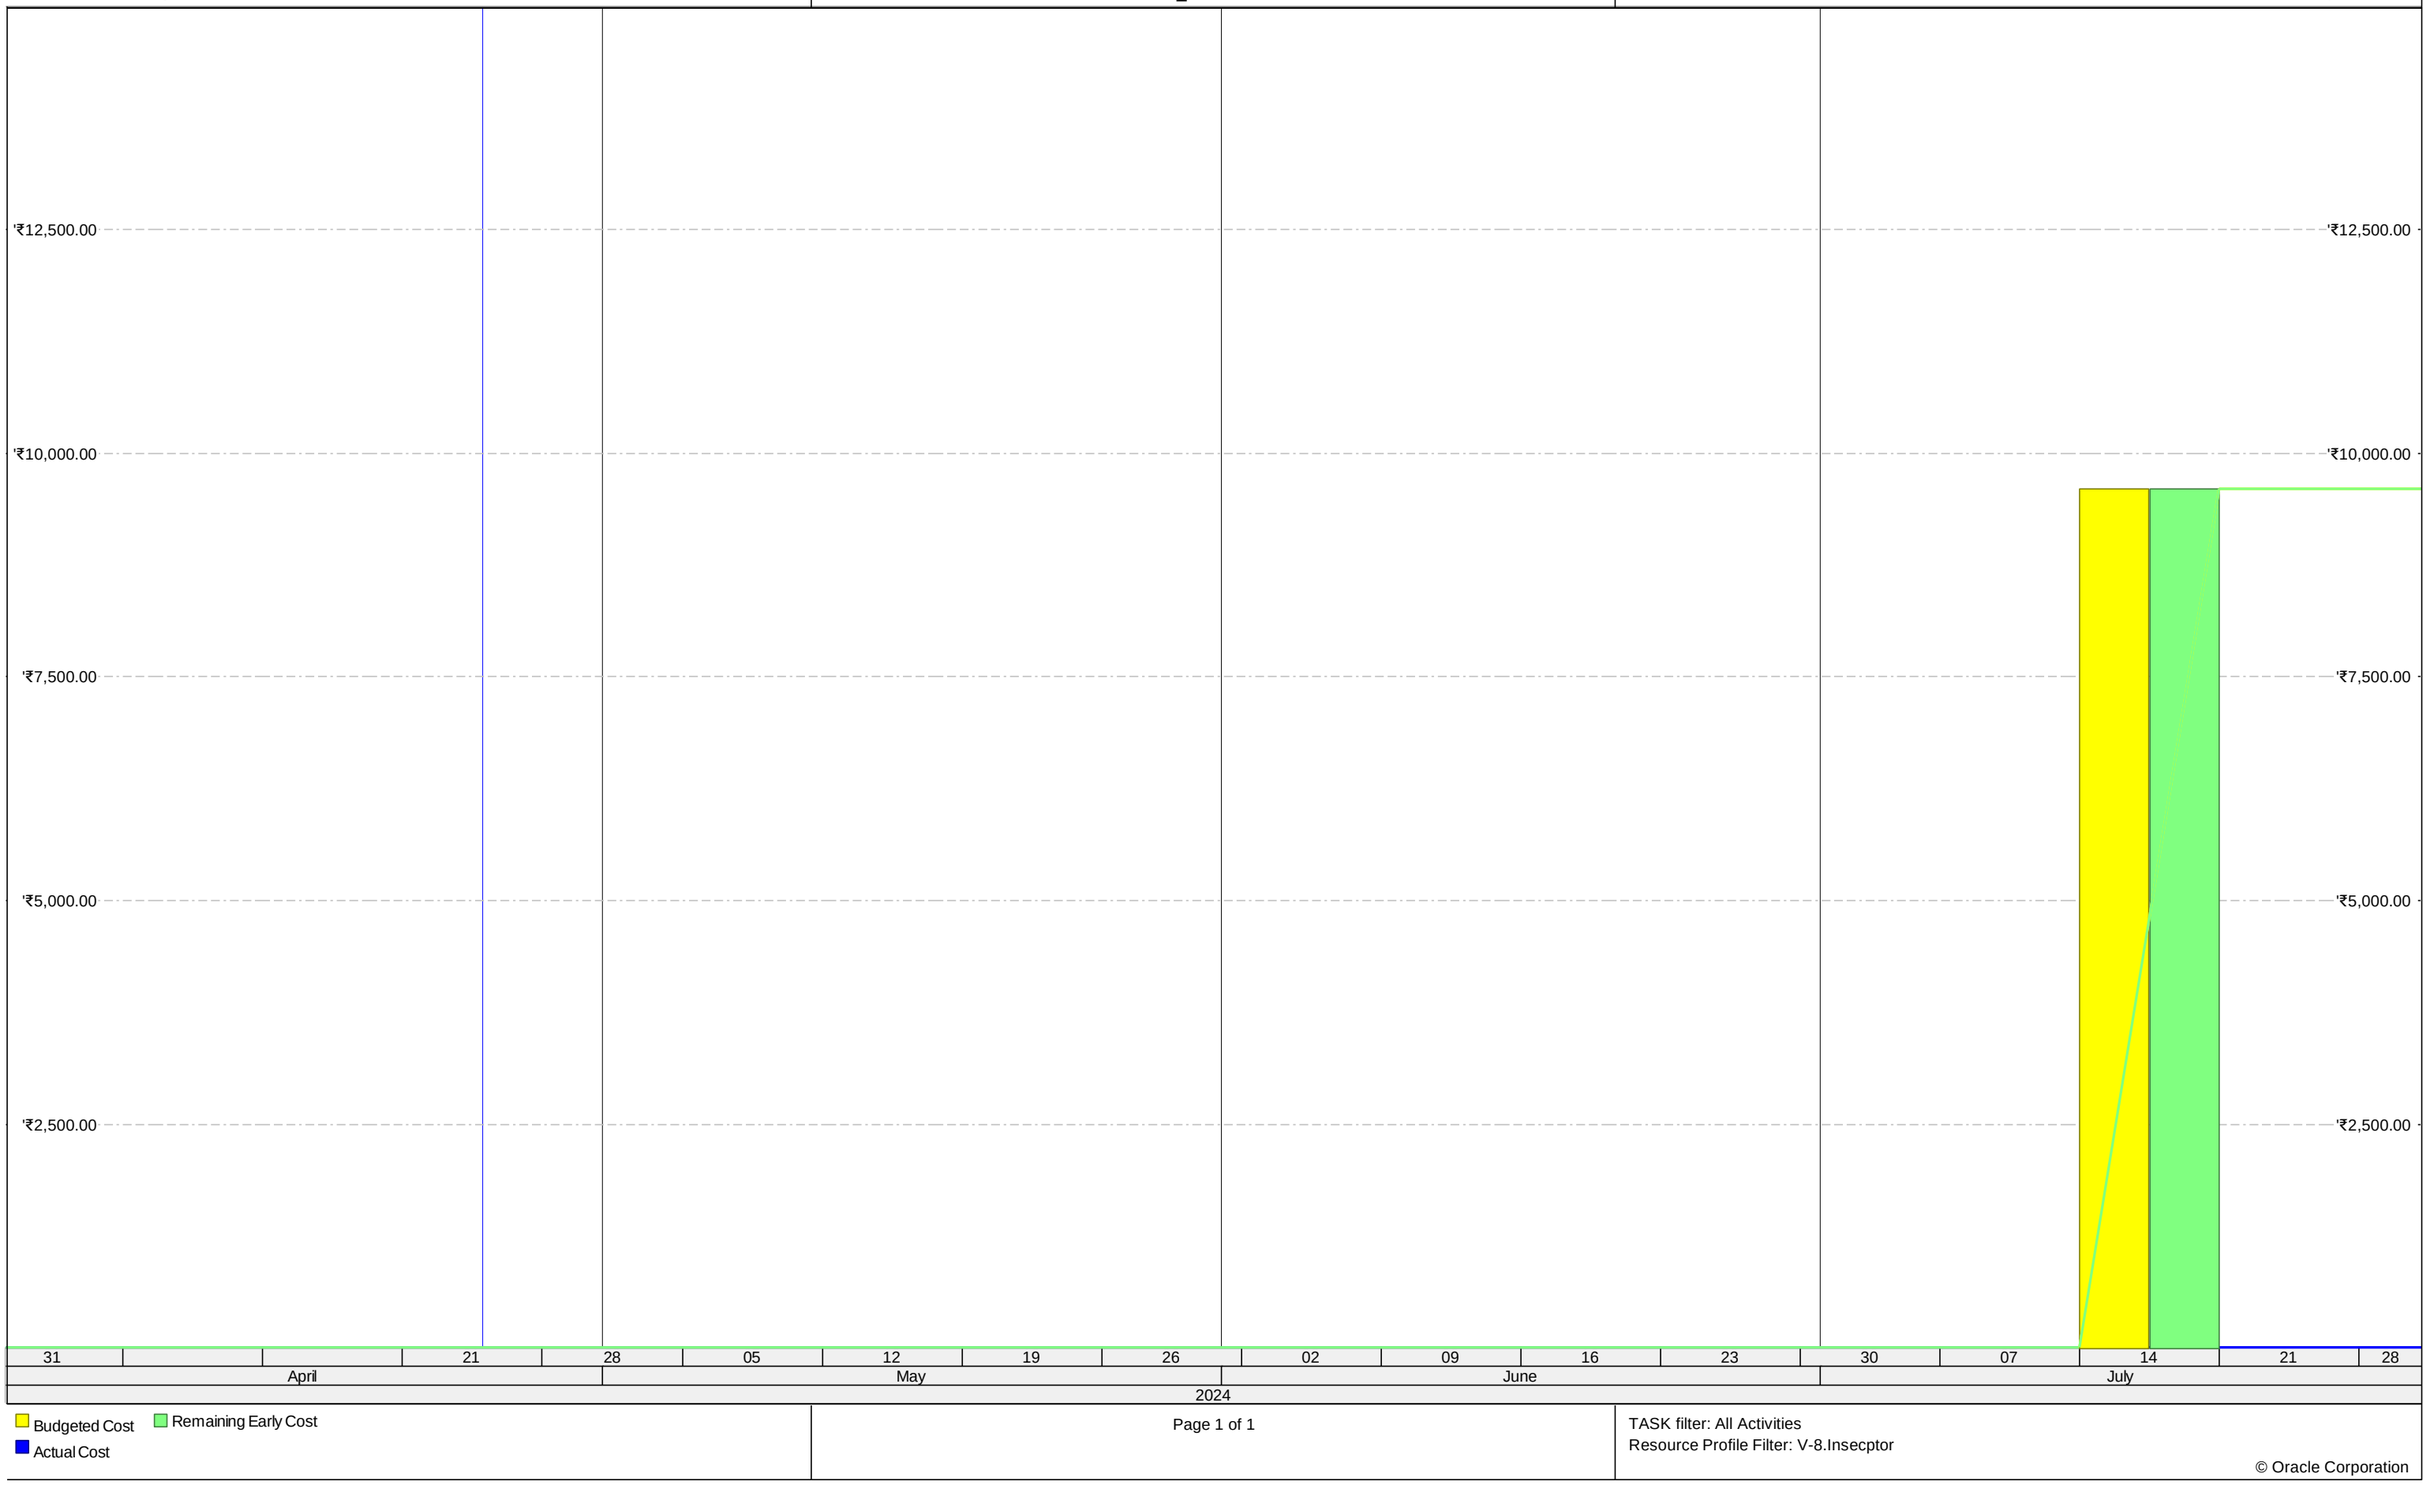

TASK filter: All Activities
Resource Profile Filter: V-8.Insecptor

© Oracle Corporation


07

14

Residential Villa Project

Concrete Blocks

30-Apr-24 05:35

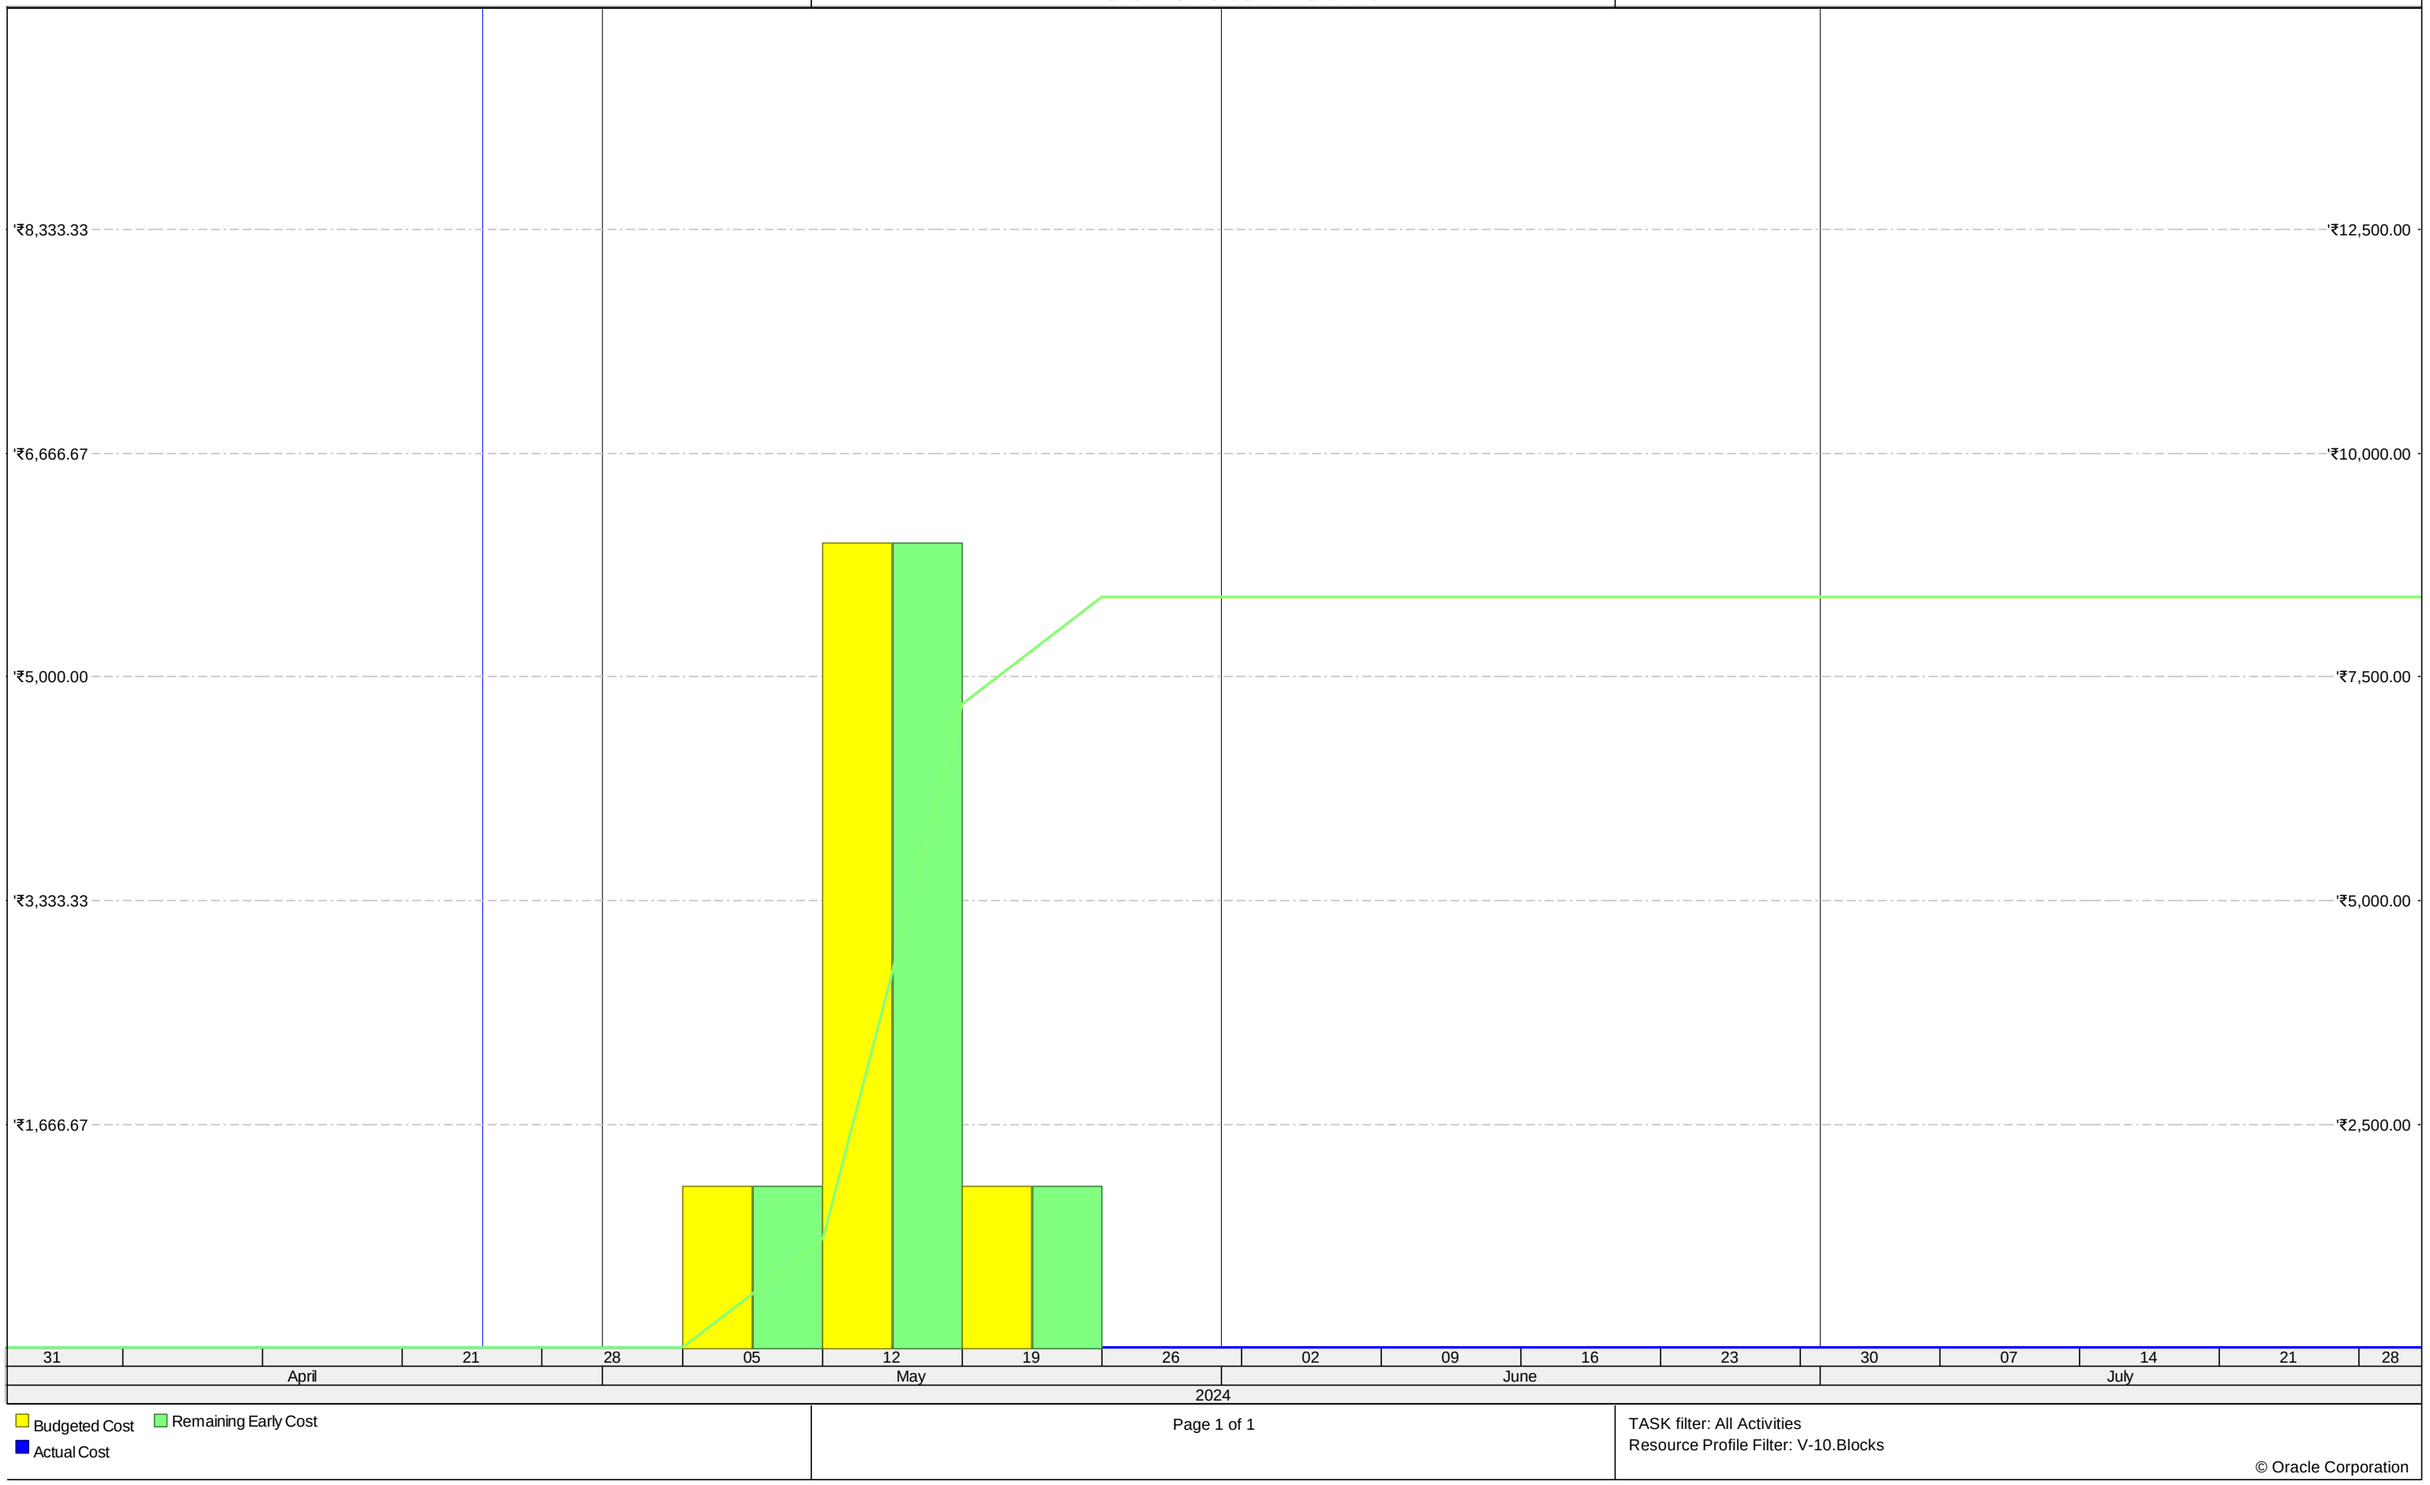

Budgeted Cost
Remaining Early Cost
Actual Cost


TASK filter: All Activities
Resource Profile Filter: V-10.Blocks

© Oracle Corporation

Cement

Residential Villa Project

30-Apr-24 05:35

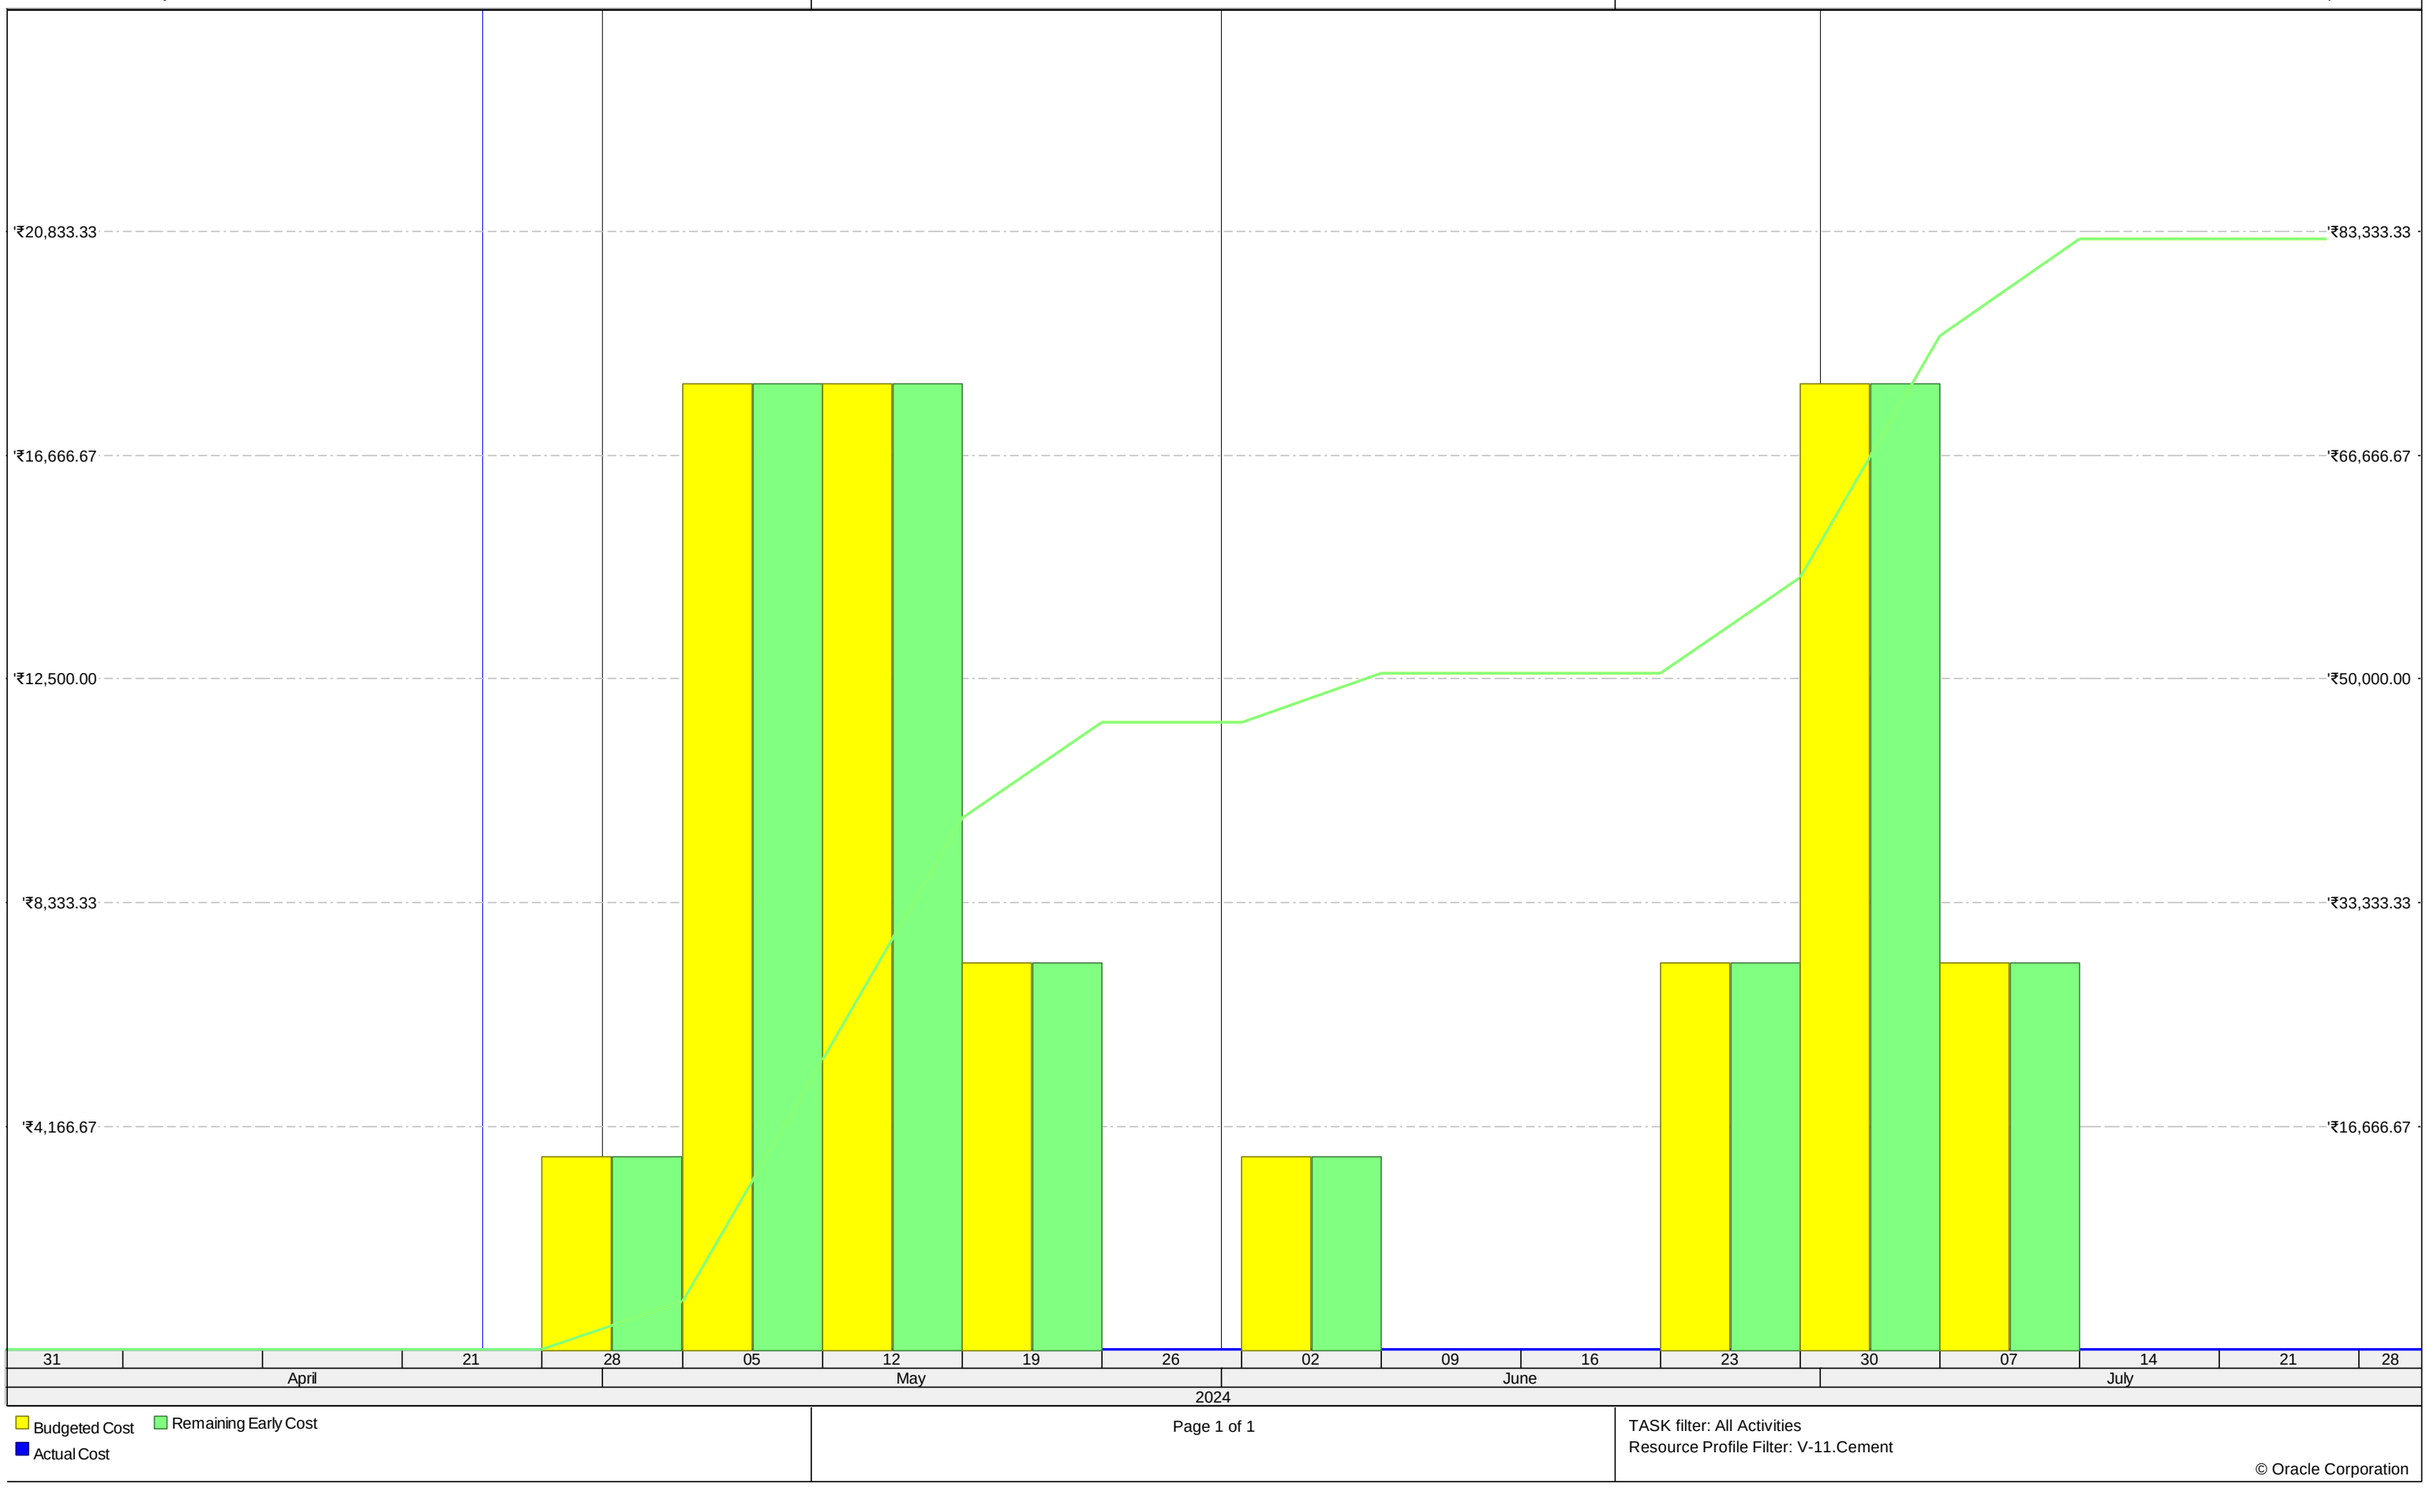

Budgeted Cost
Remaining Early Cost
Actual Cost

Page 1 of 1

TASK filter: All Activities
Resource Profile Filter: V-11.Cement

© Oracle Corporation


07

14

Paint

Residential Villa Project

30-Apr-24 05:35

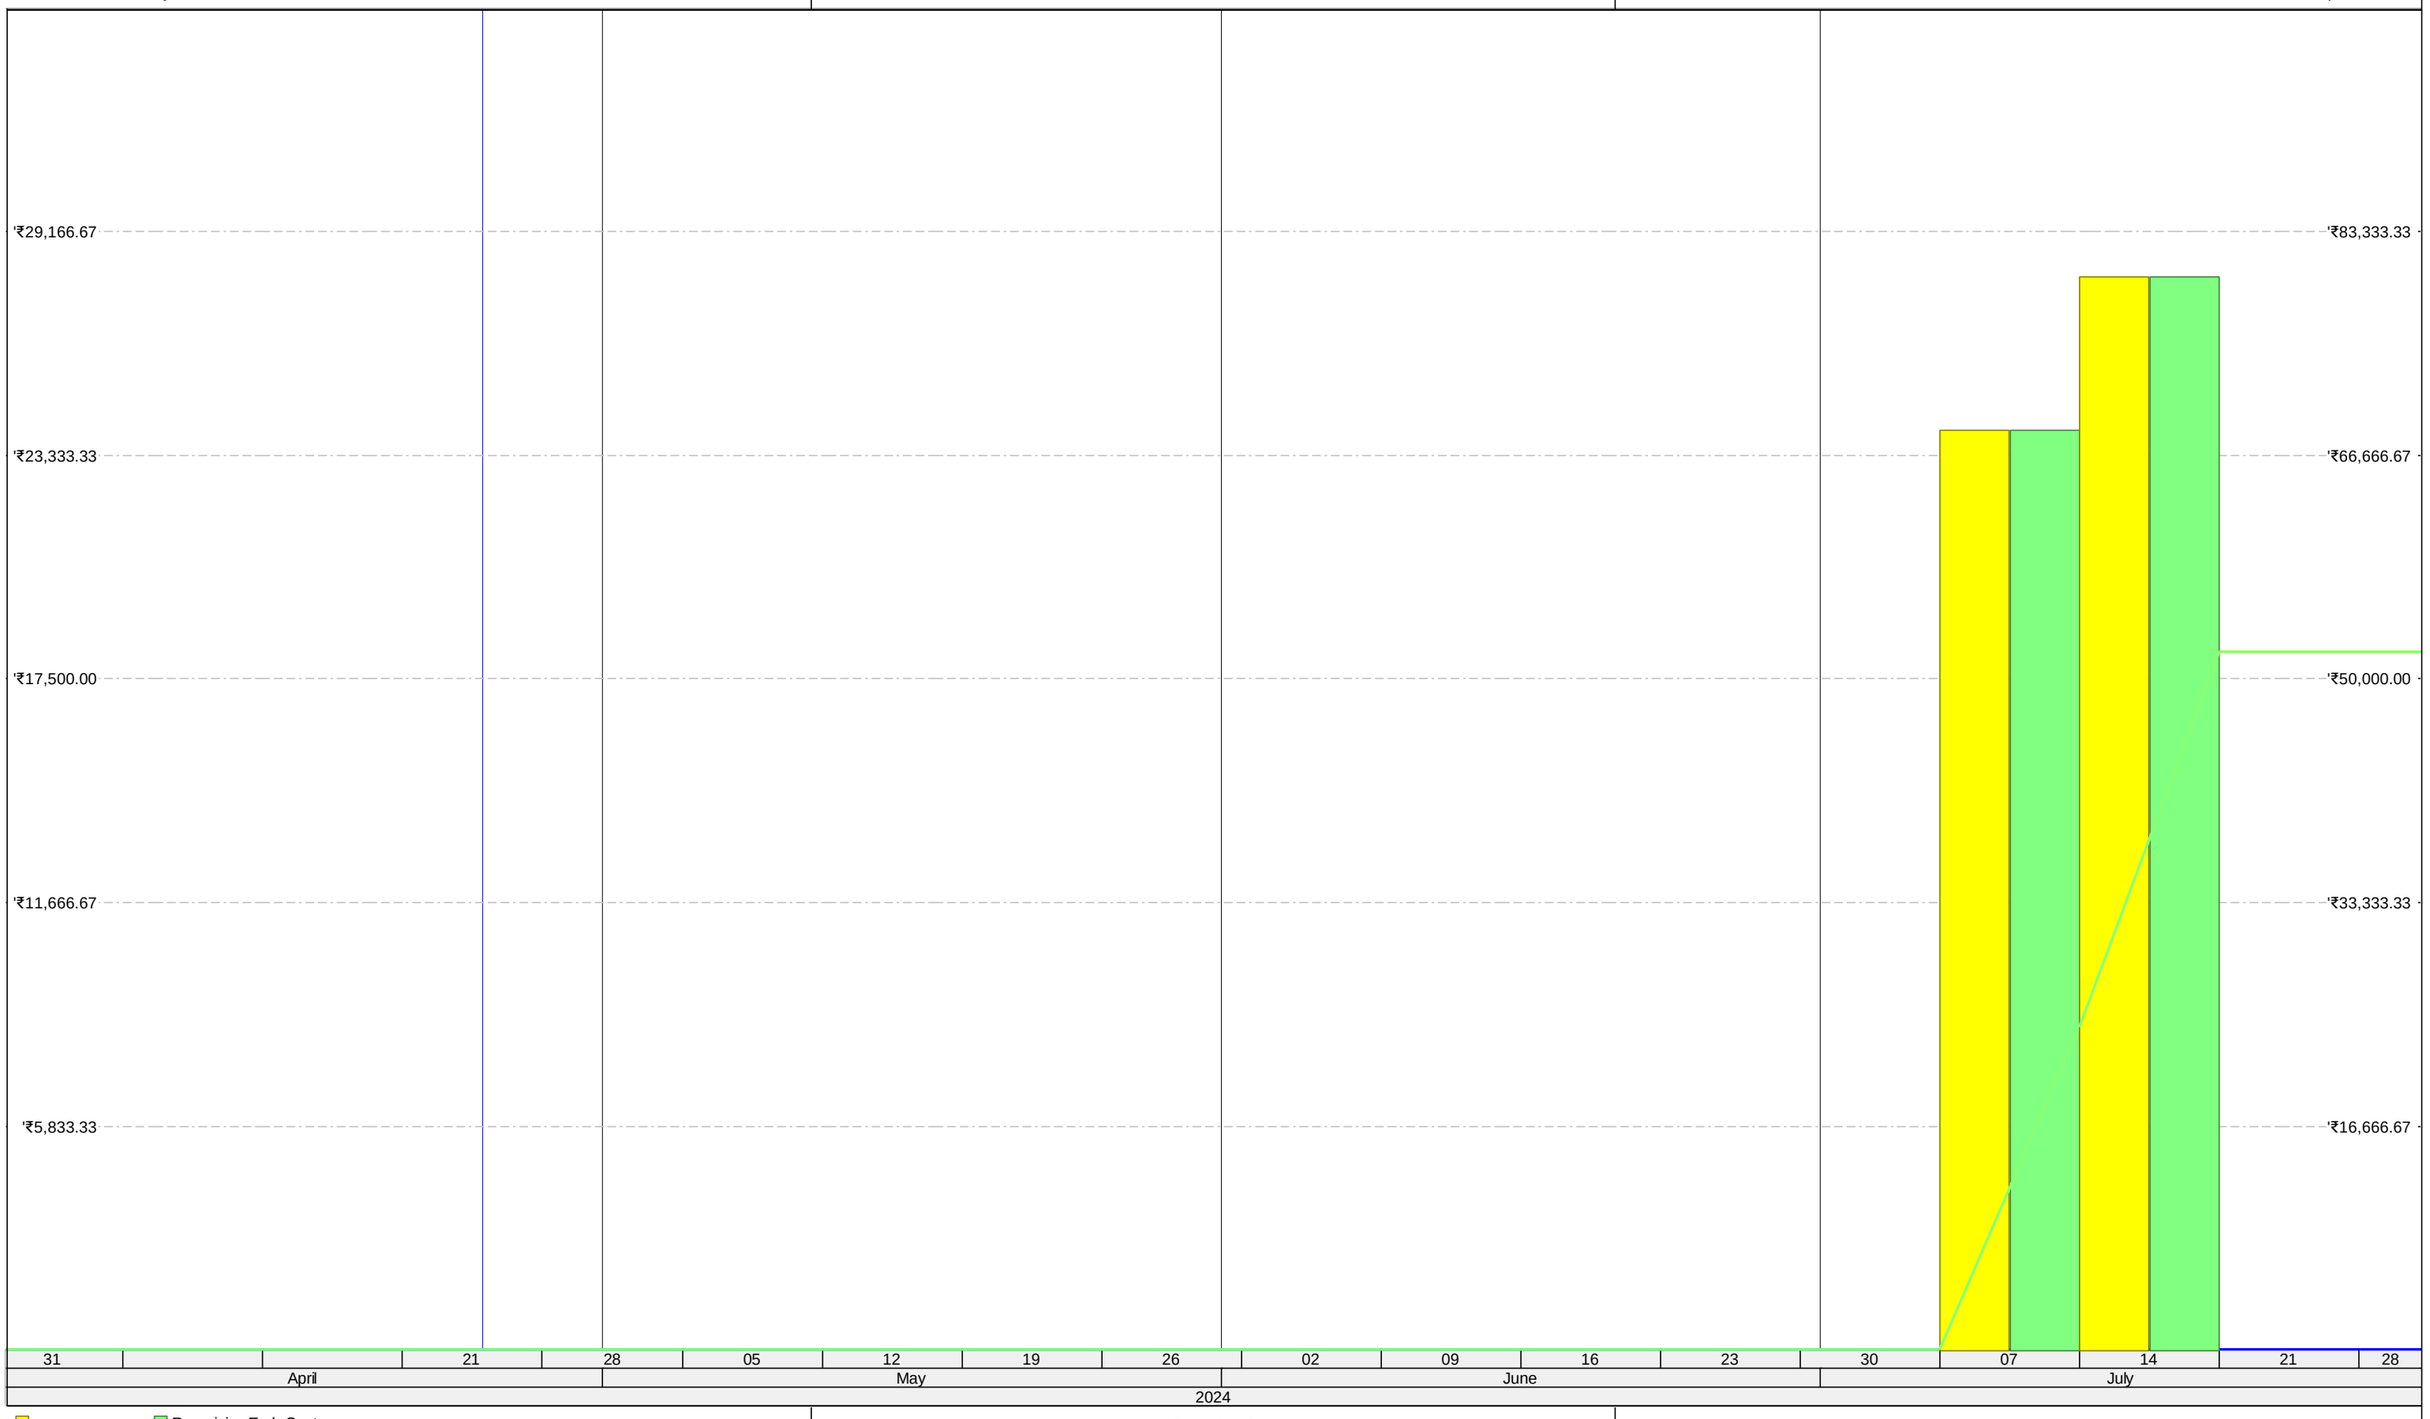

Budgeted Cost
Remaining Early Cost
Actual Cost

TASK filter: All Activities
Resource Profile Filter: V-12.Paint

© Oracle Corporation


07

14

Residential Villa Project

Sand

30-Apr-24 05:36

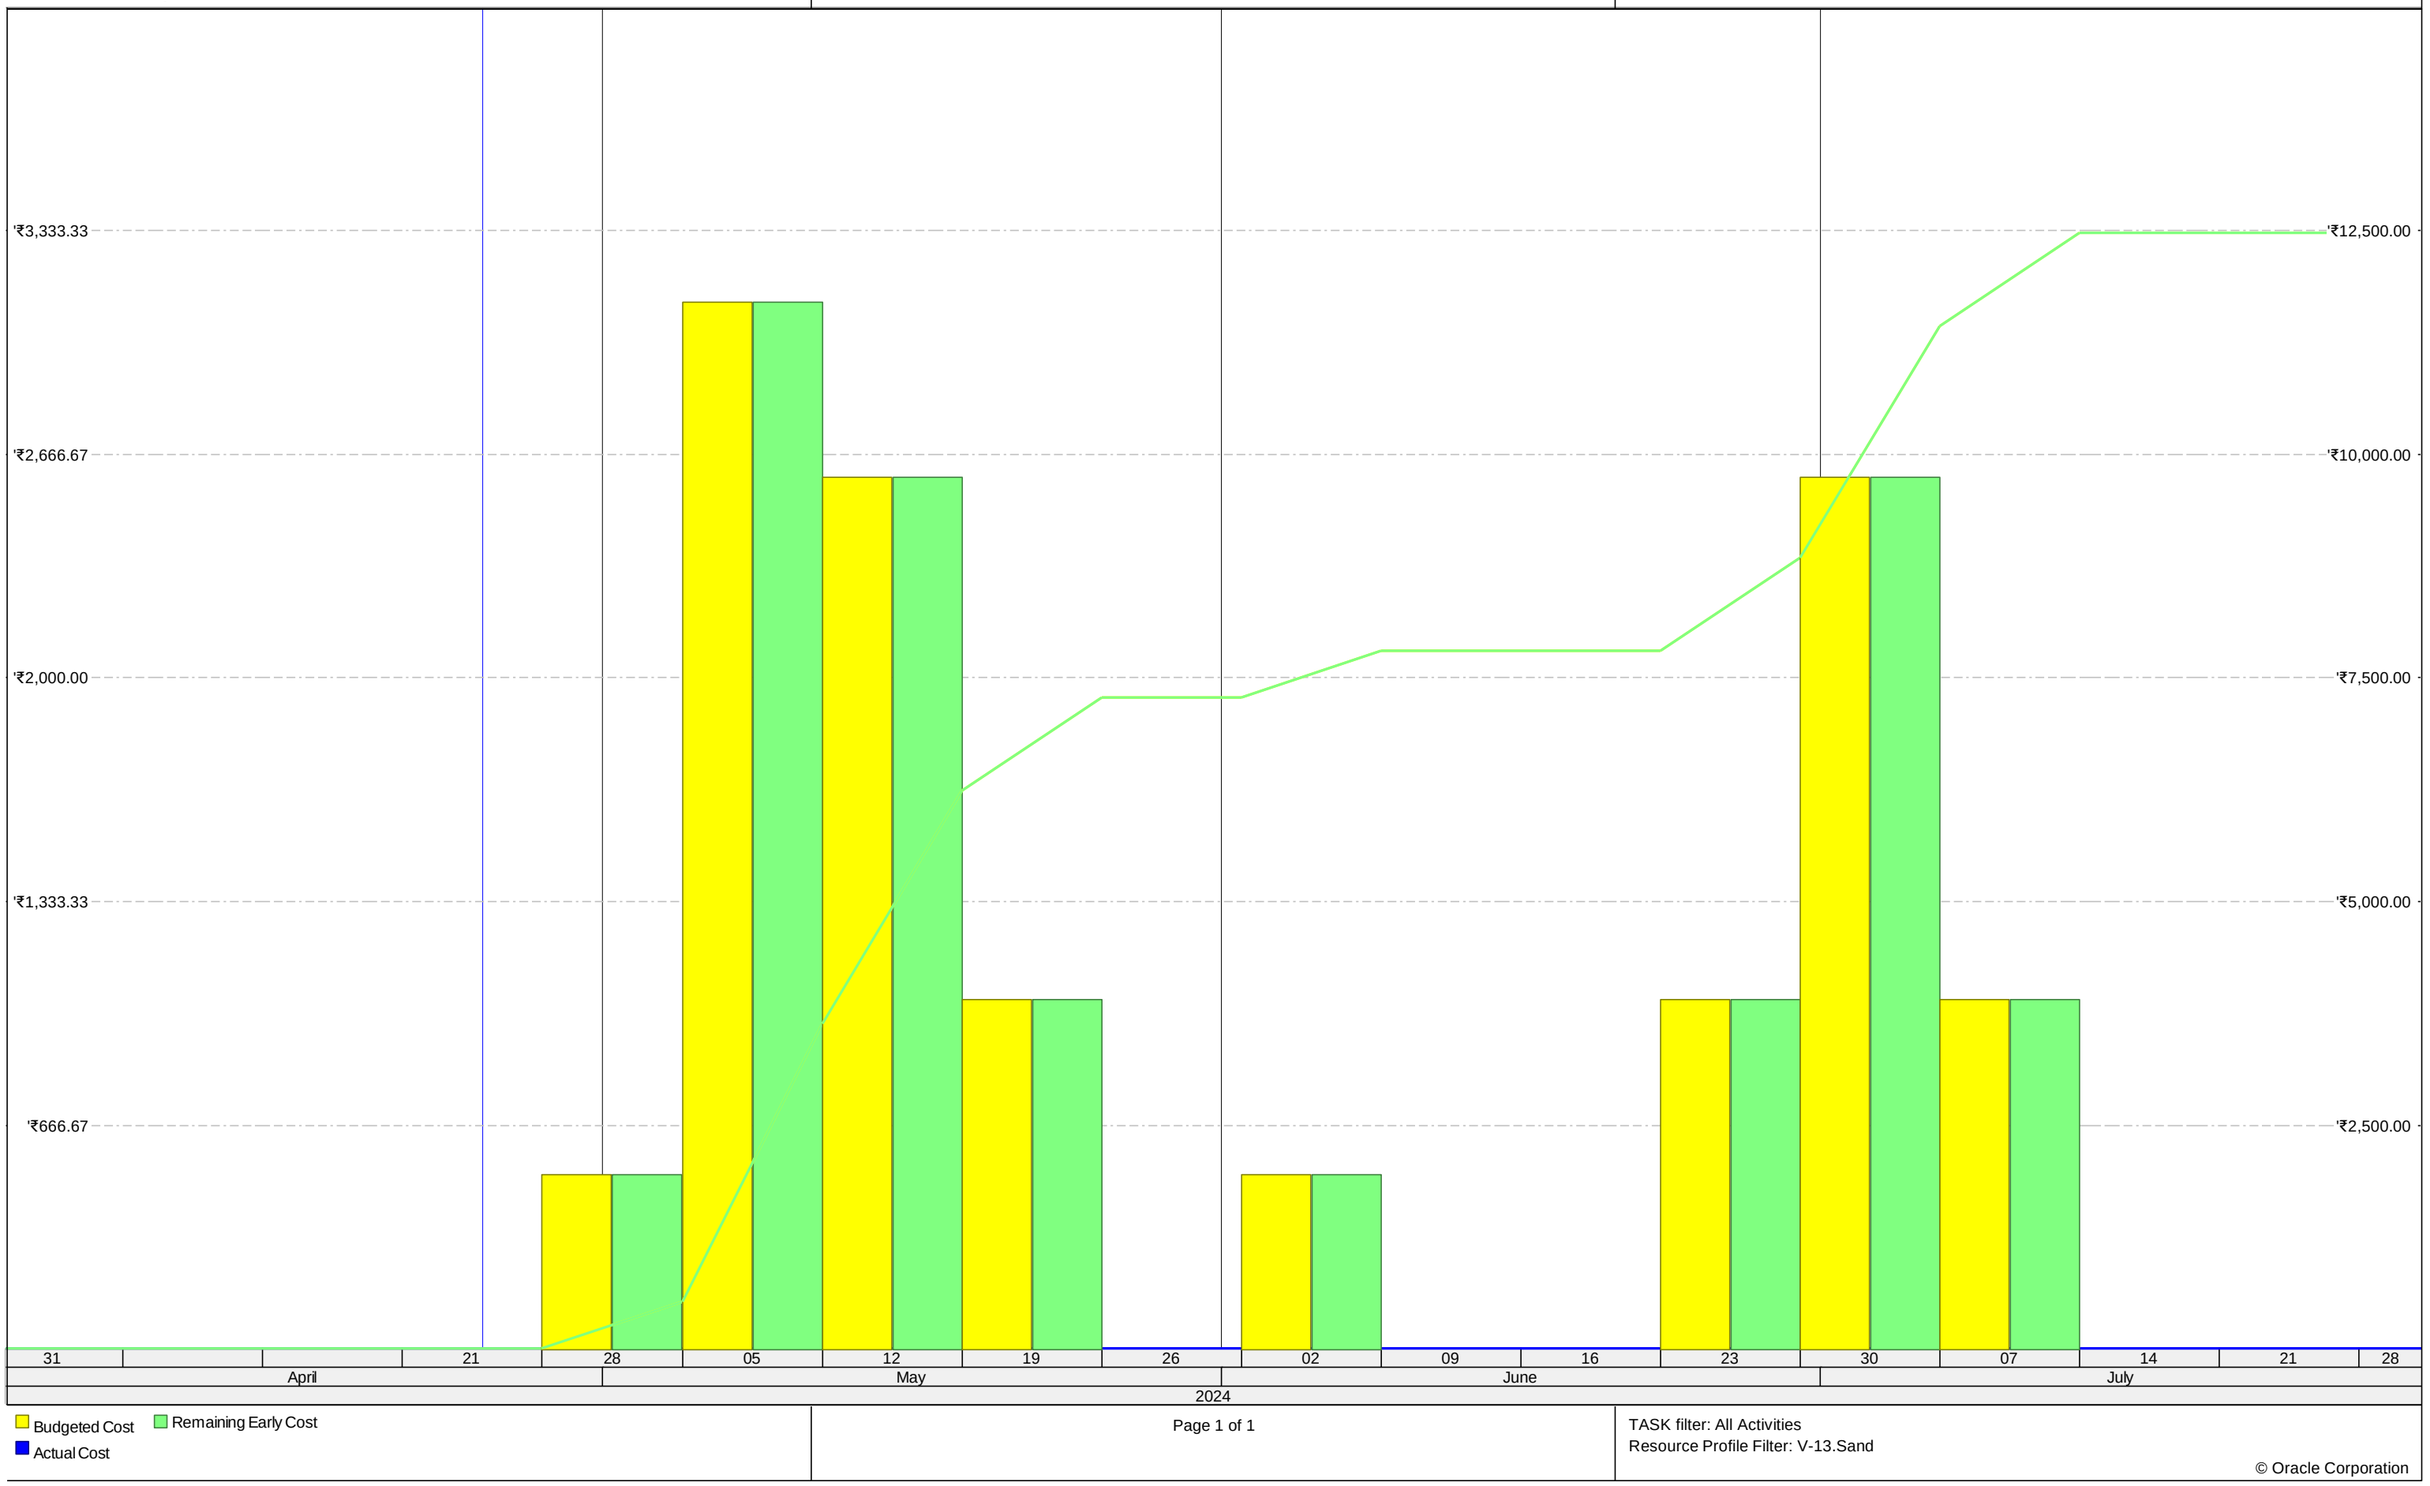

Budgeted Cost
Remaining Early Cost
Actual Cost

TASK filter: All Activities
Resource Profile Filter: V-13.Sand

© Oracle Corporation


07

14

Residential Villa Project

Steel

30-Apr-24 05:36

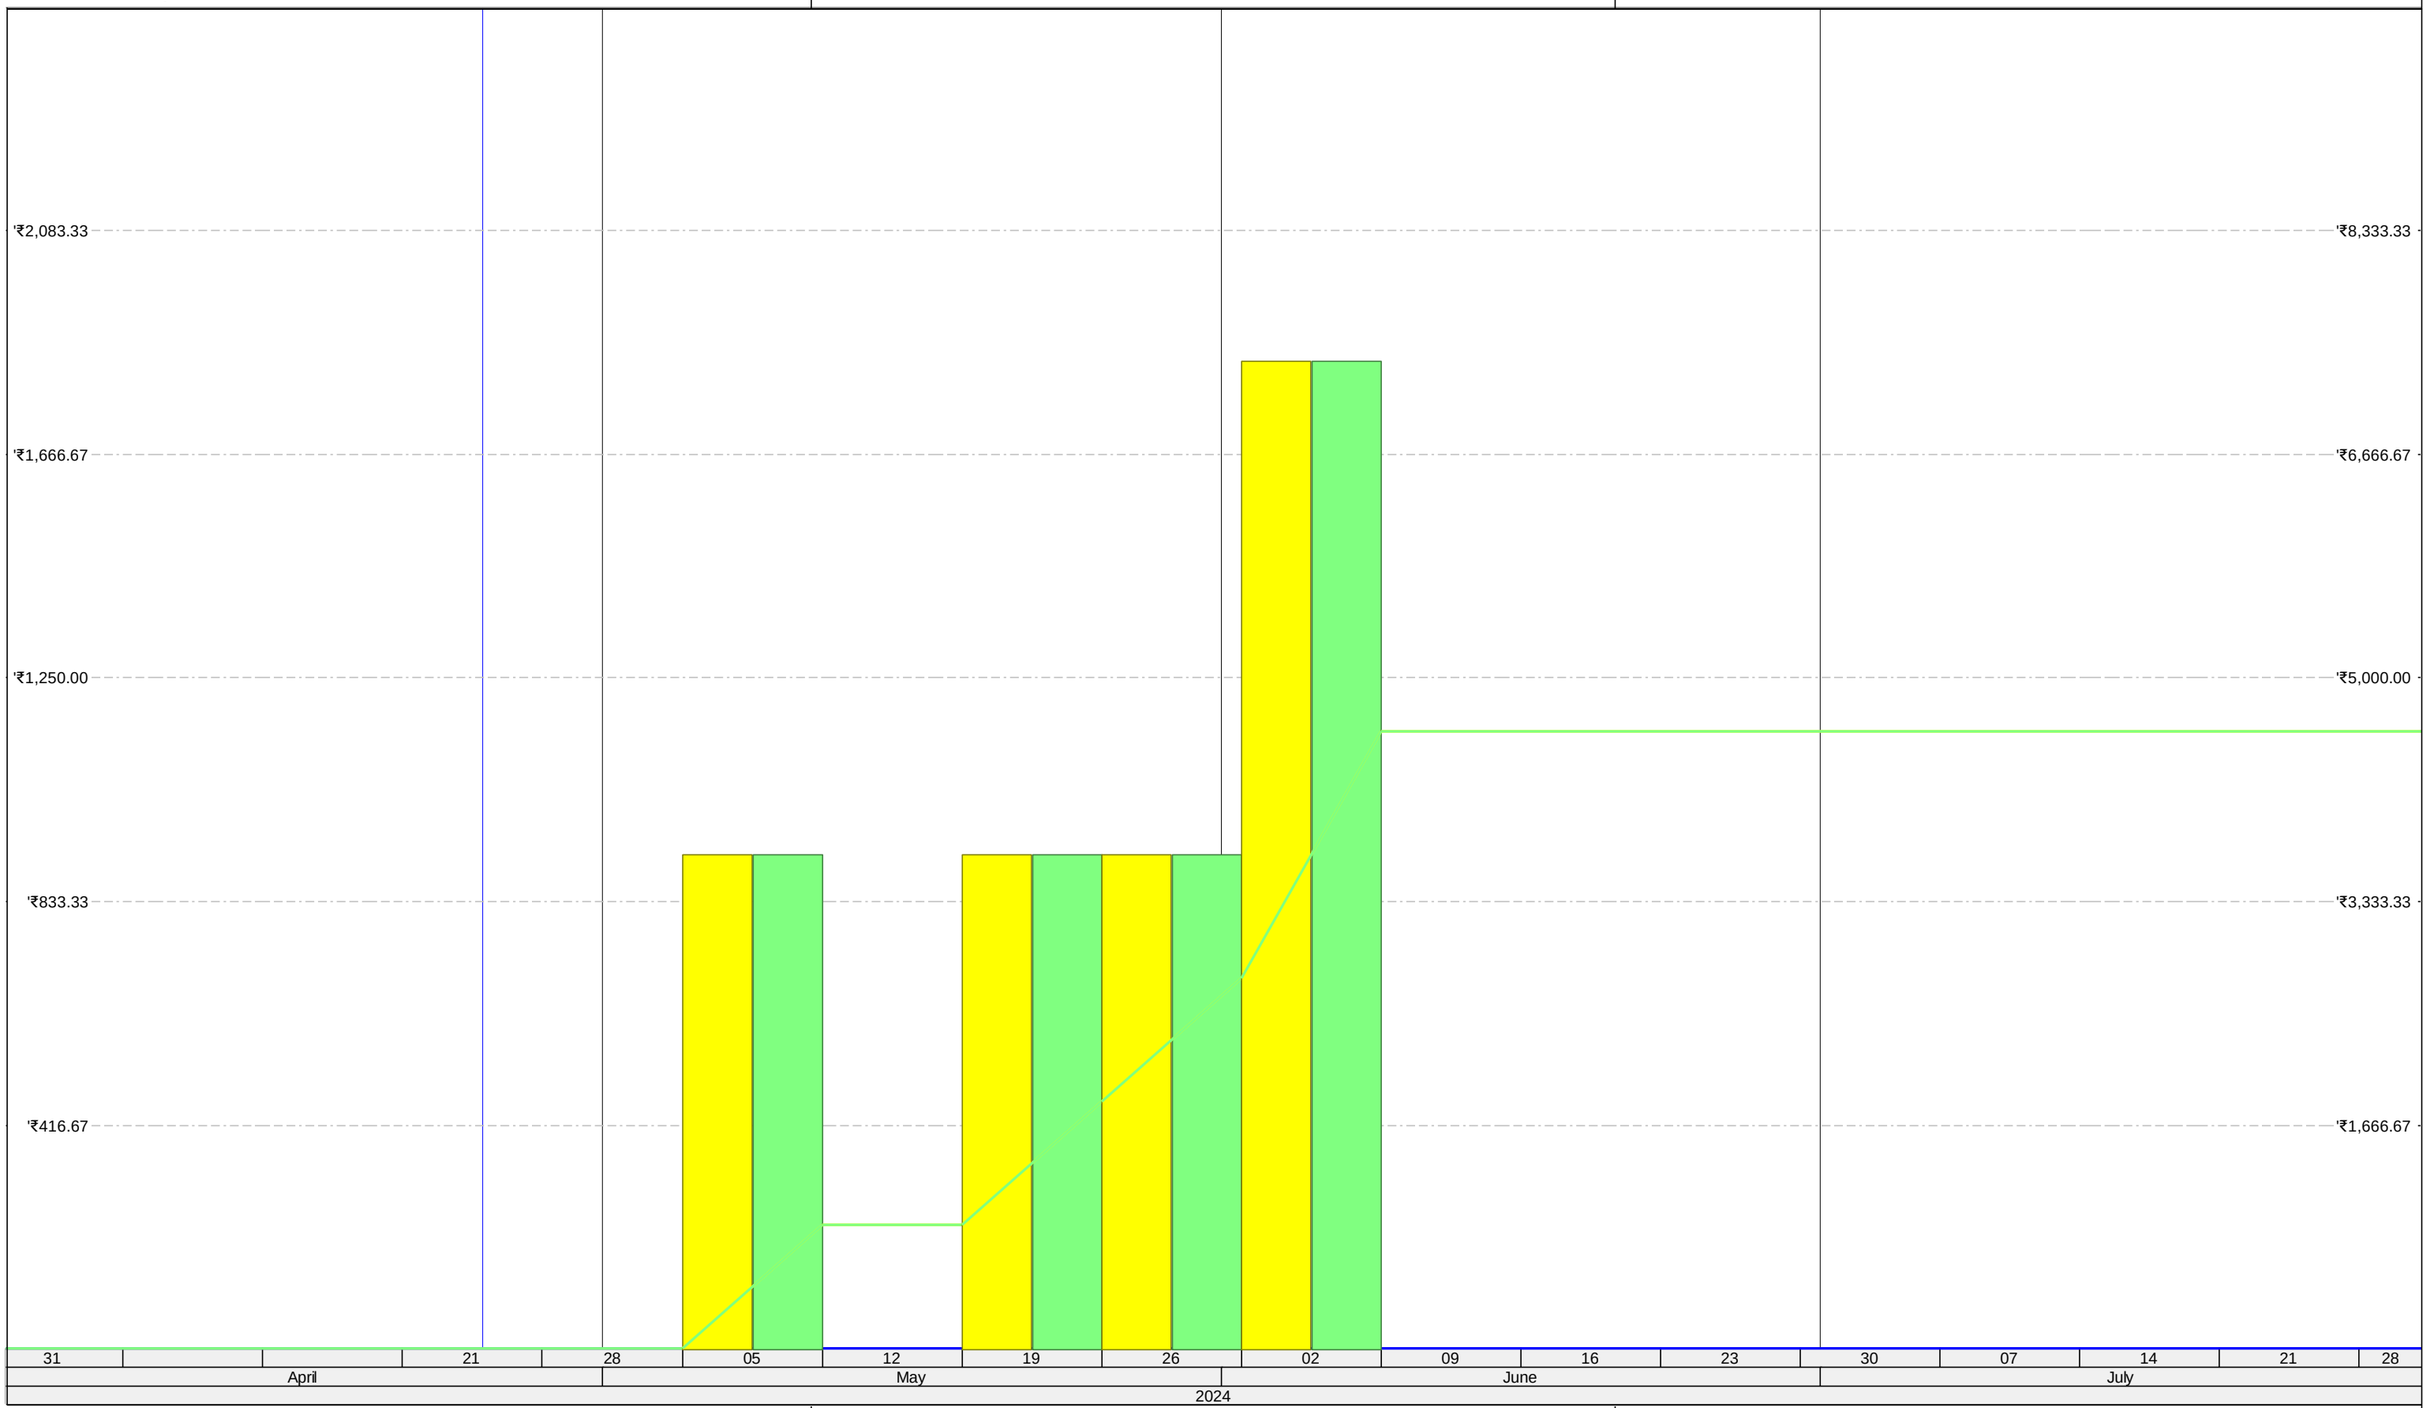

TASK filter: All Activities
Resource Profile Filter: V-14.Steel

© Oracle Corporation


07

14

Residential Villa Project

Wood/Lintels

30-Apr-24 05:36

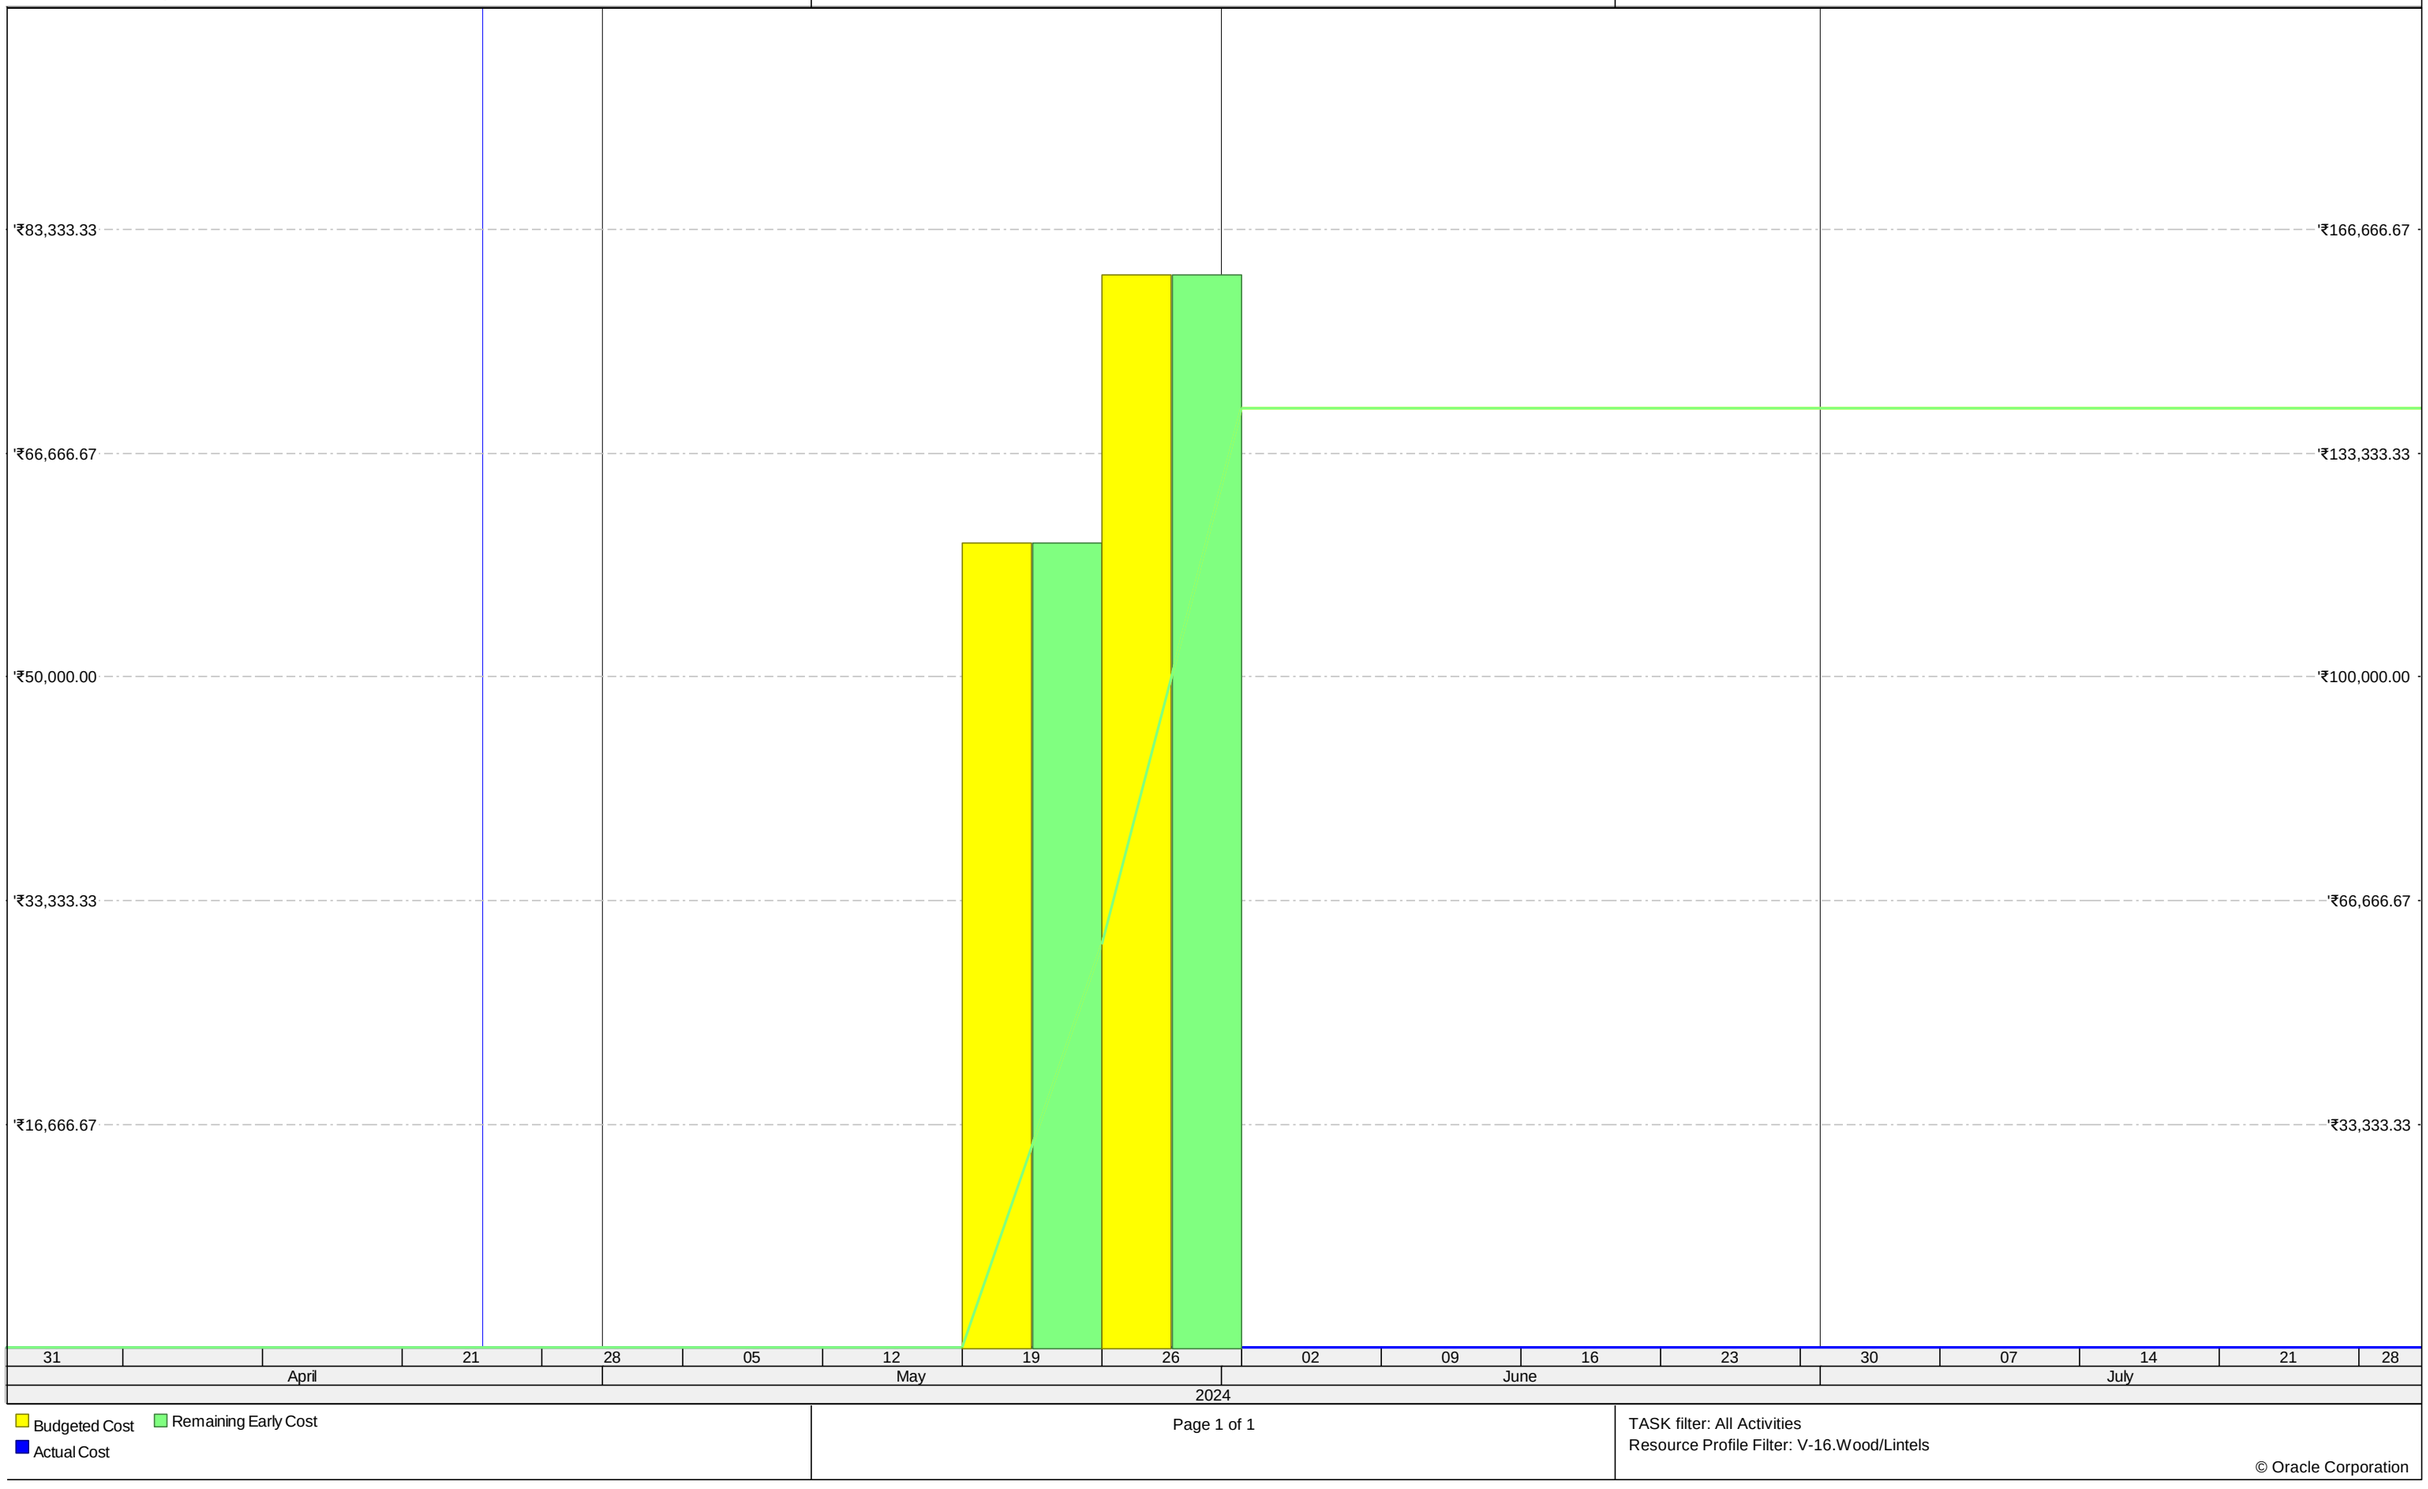

Budgeted Cost
Remaining Early Cost
Actual Cost


TASK filter: All Activities
Resource Profile Filter: V-16.Wood/Lintels

© Oracle Corporation

Residential Villa Project

Concrete Crushes

30-Apr-24 05:37

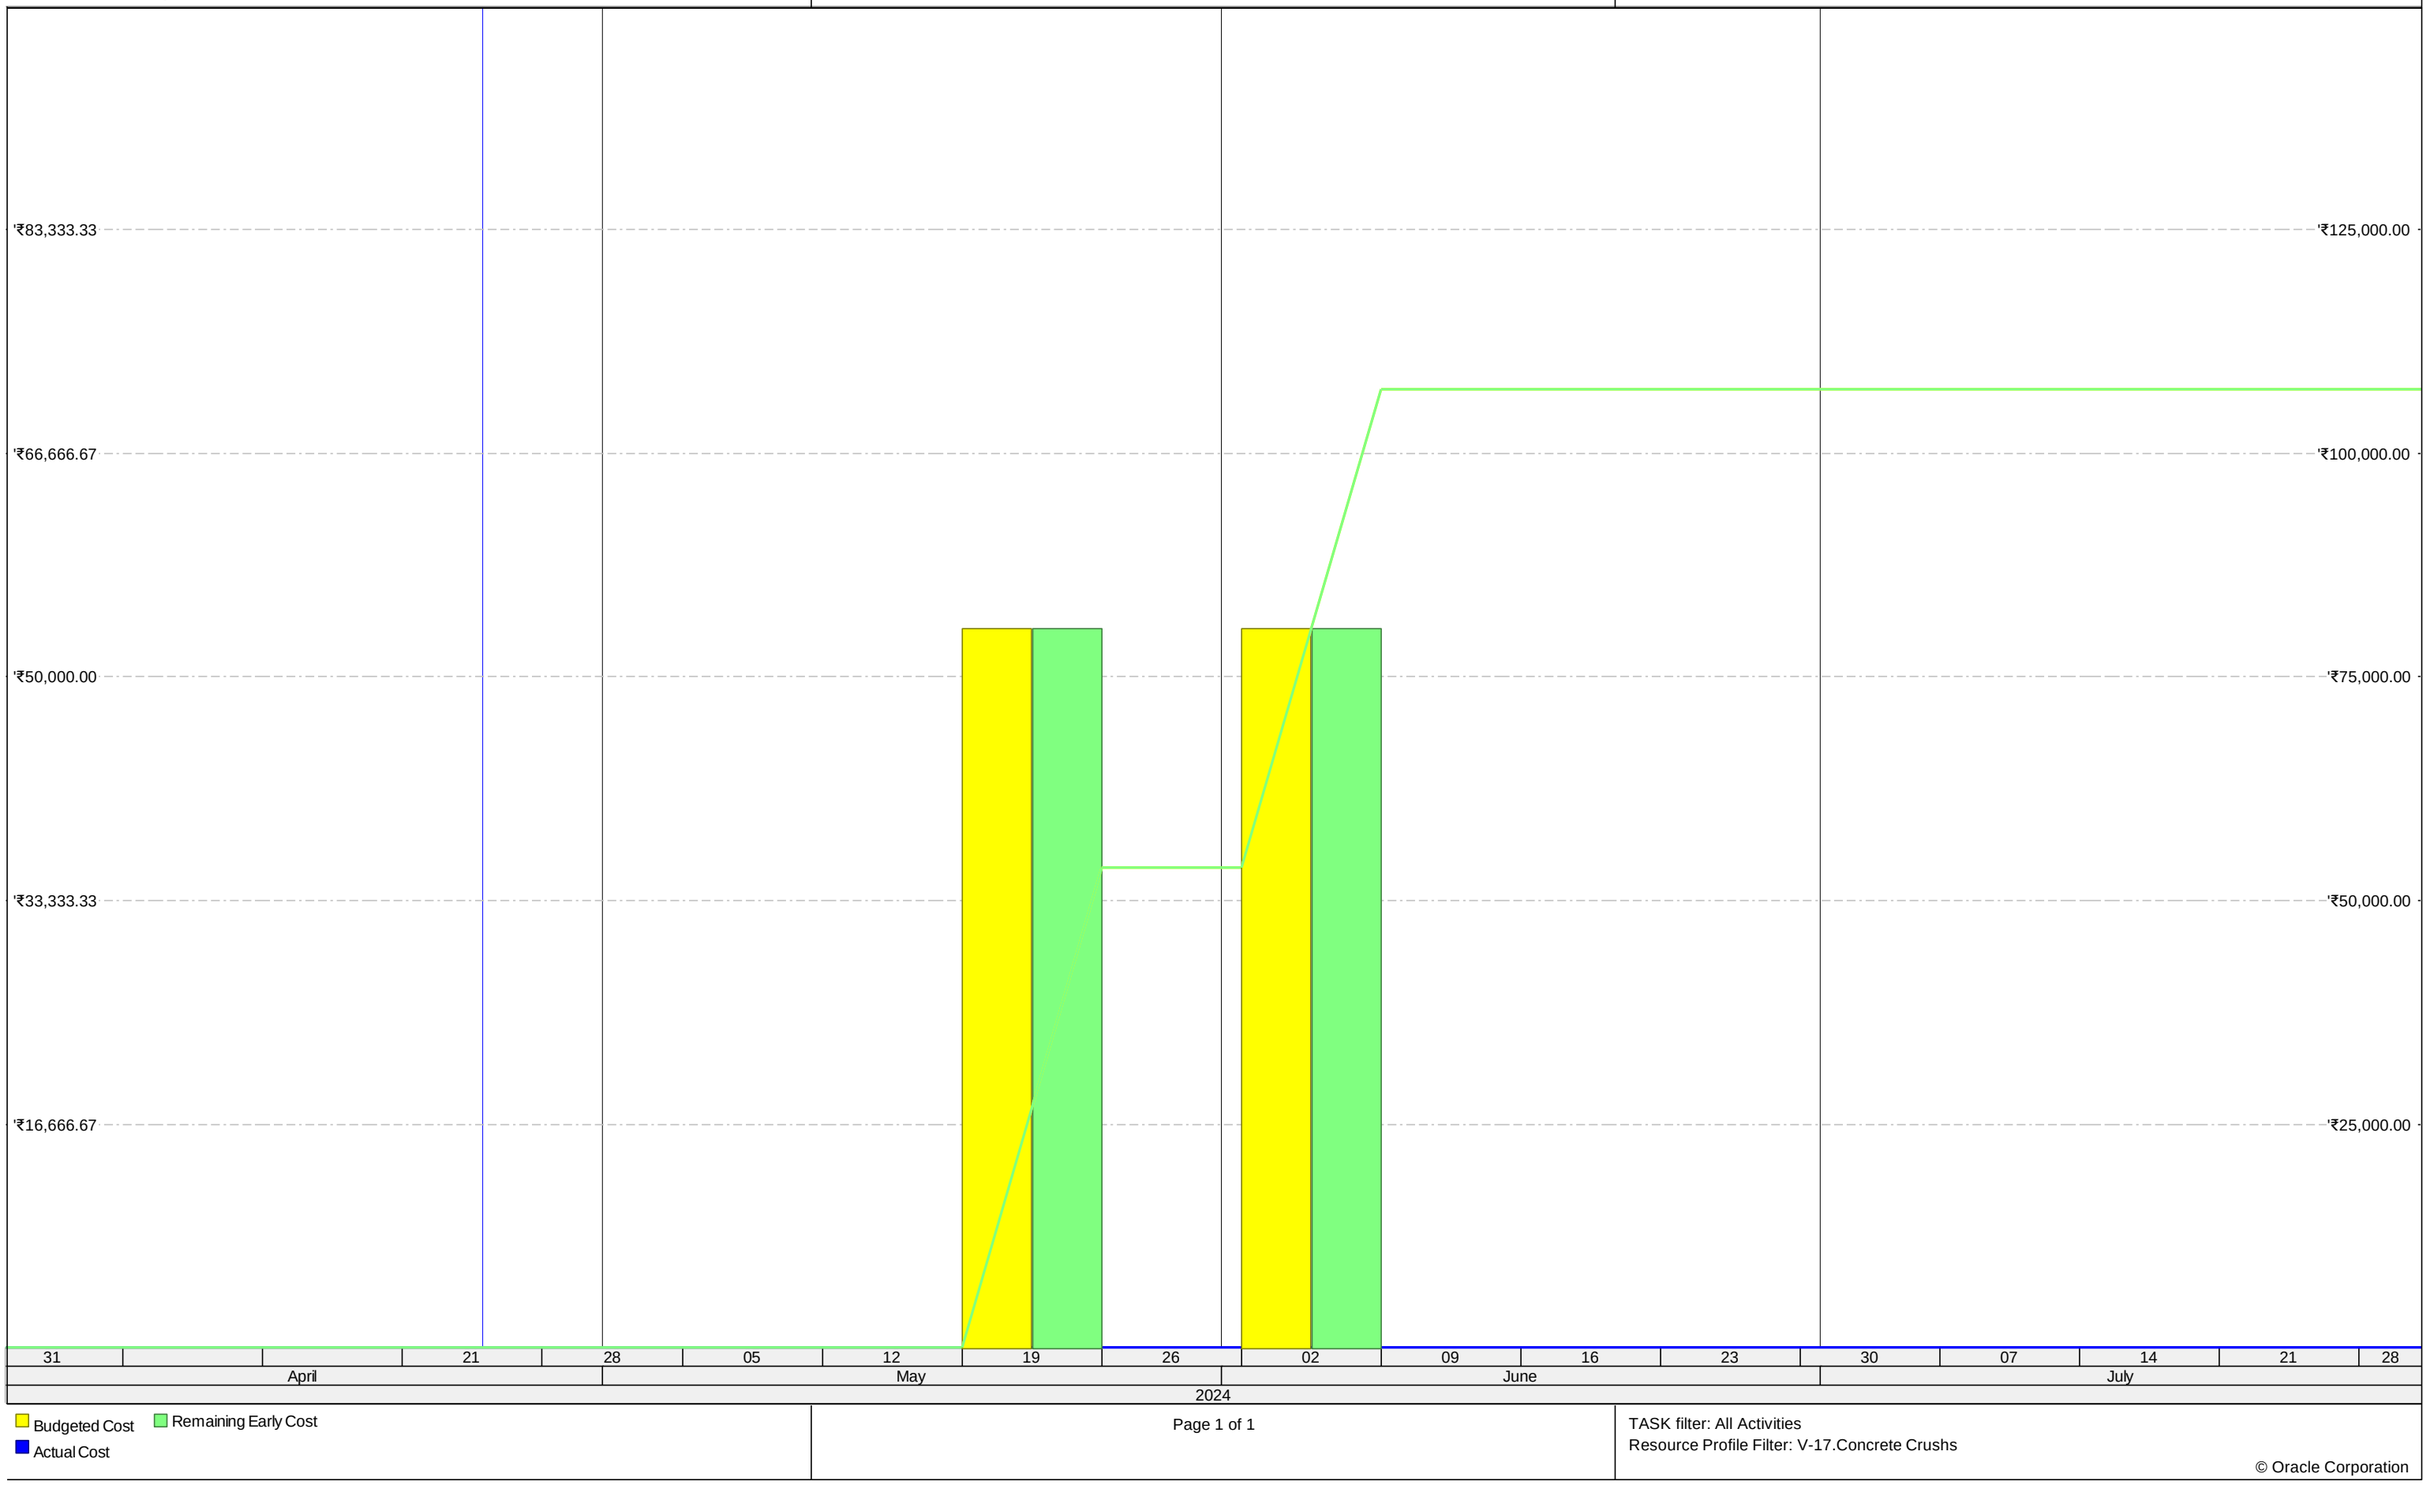

Budgeted Cost
Remaining Early Cost
Actual Cost


TASK filter: All Activities
Resource Profile Filter: V-17.Concrete Crushs

© Oracle Corporation

Residential Villa Project

JCB

30-Apr-24 05:37

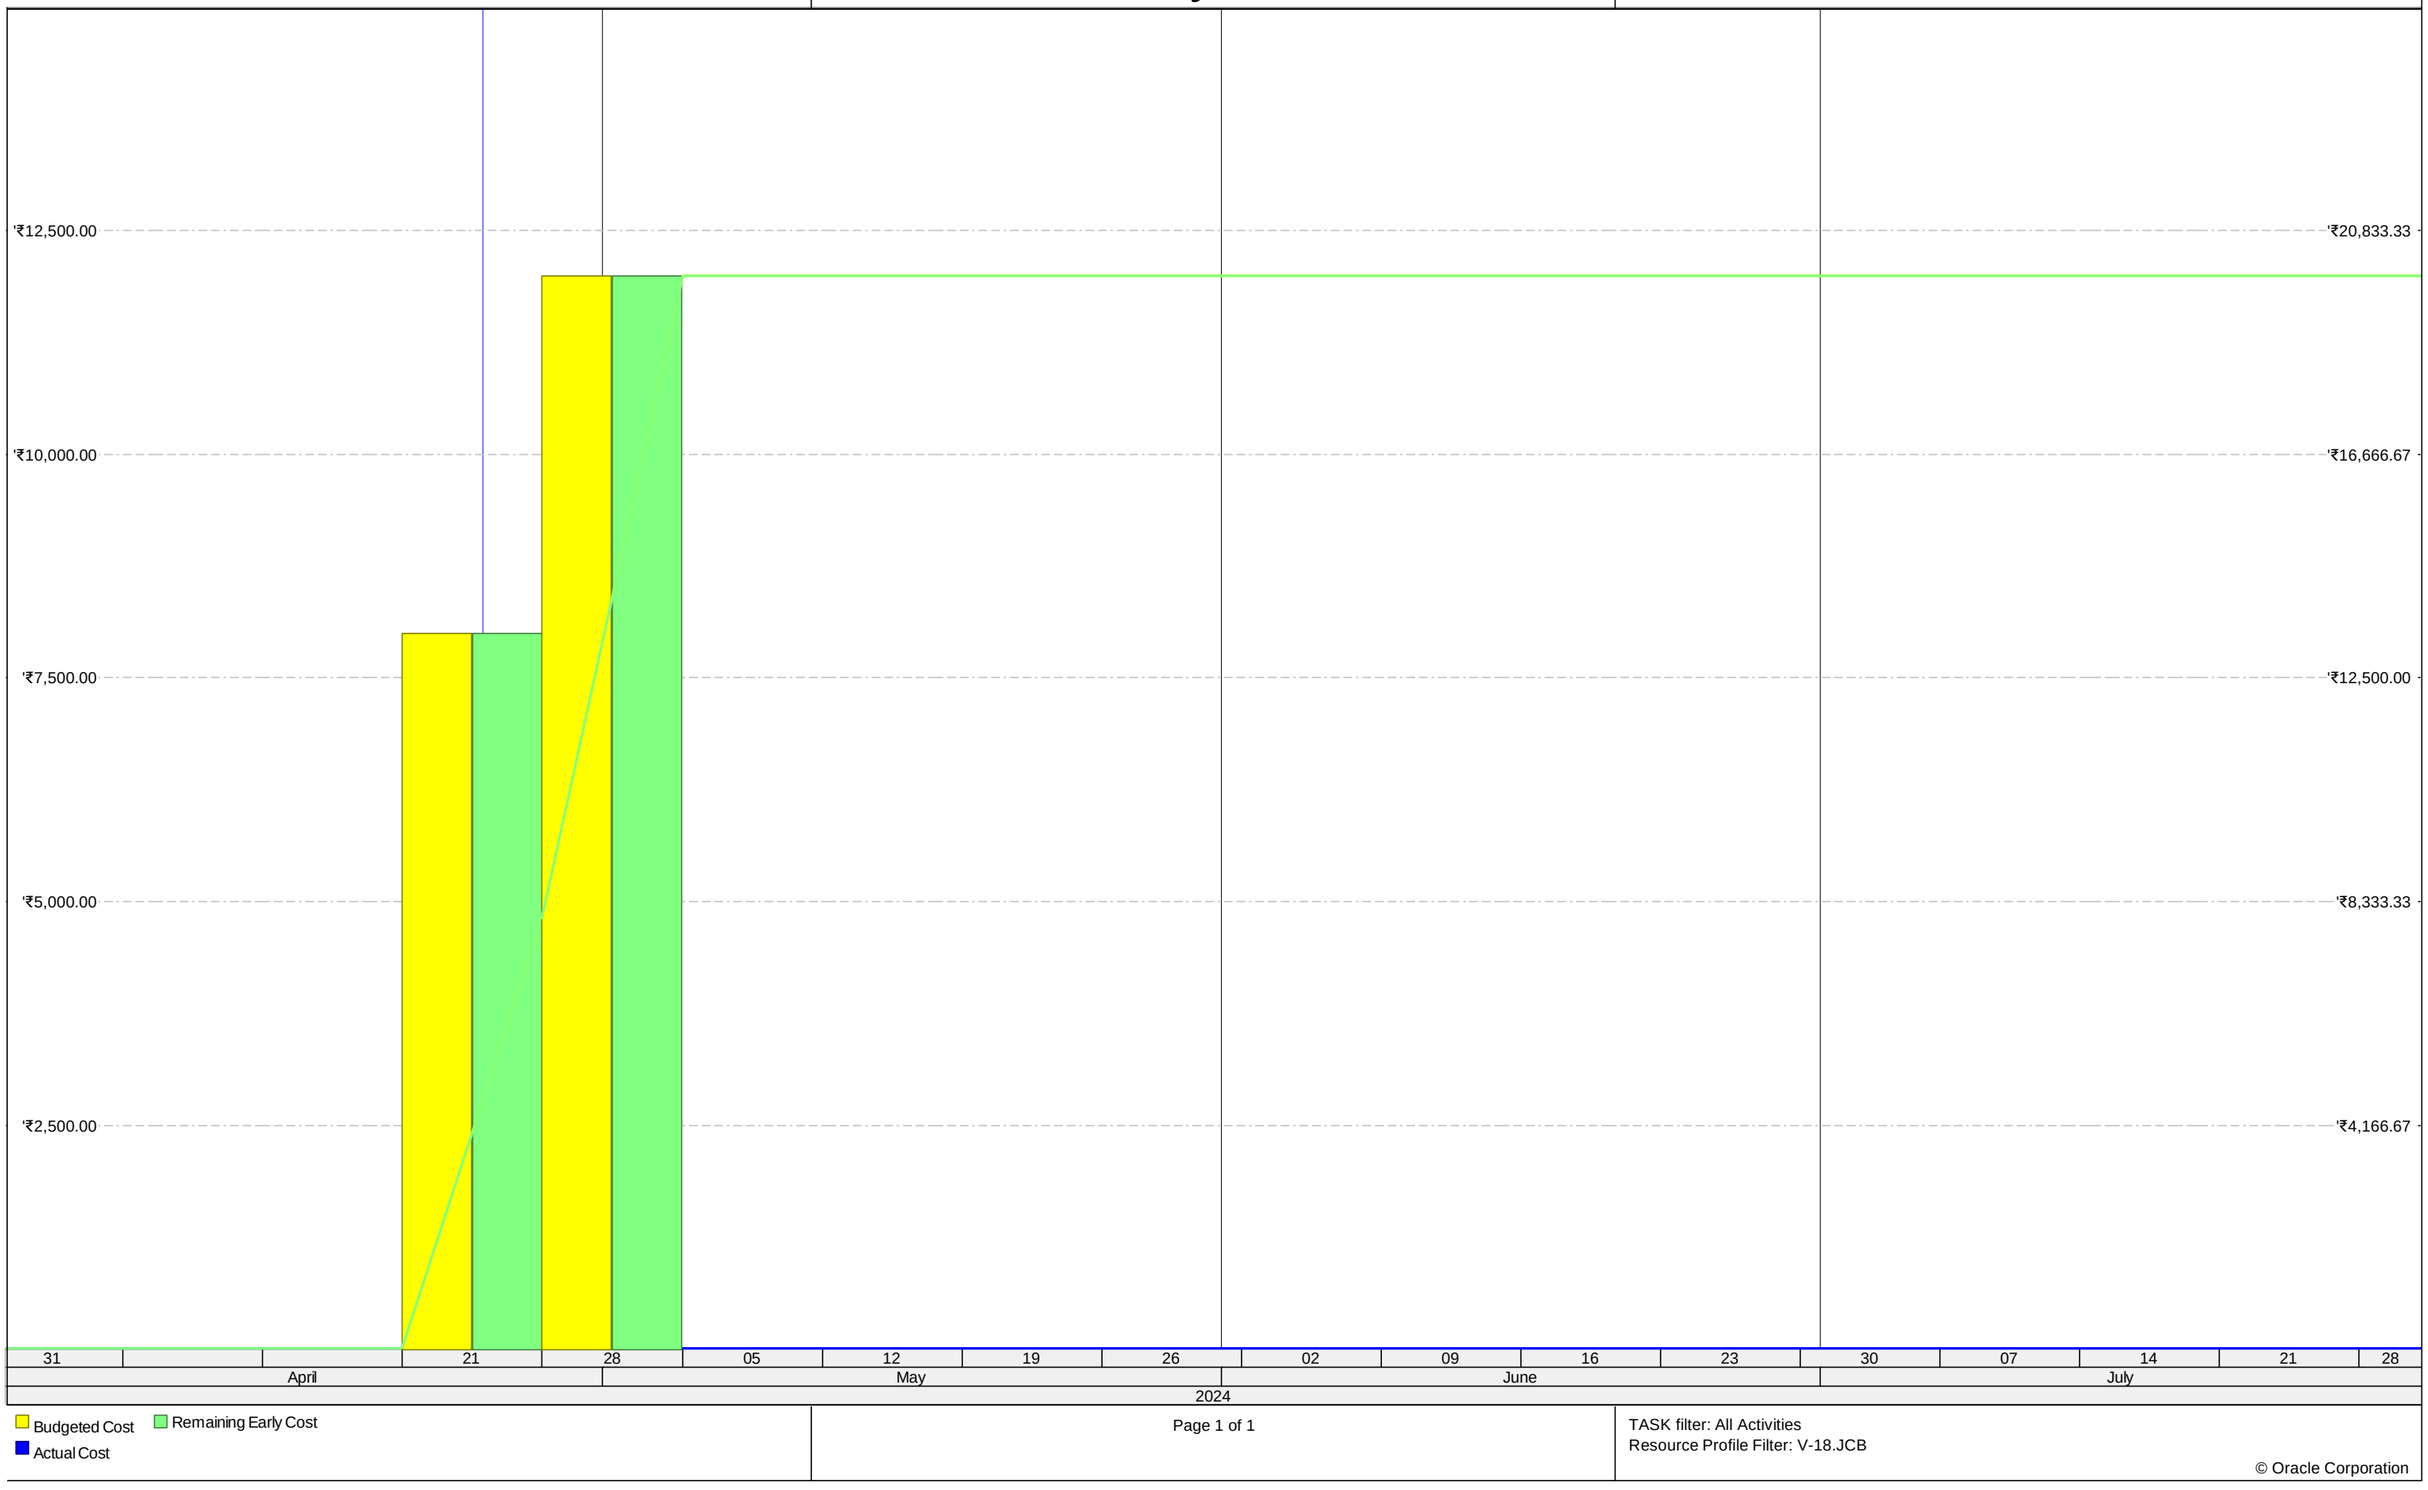

Page 1 of 1


TASK filter: All Activities
Resource Profile Filter: V-18.JCB

© Oracle Corporation

Residential Villa Project

Excavator

30-Apr-24 05:37

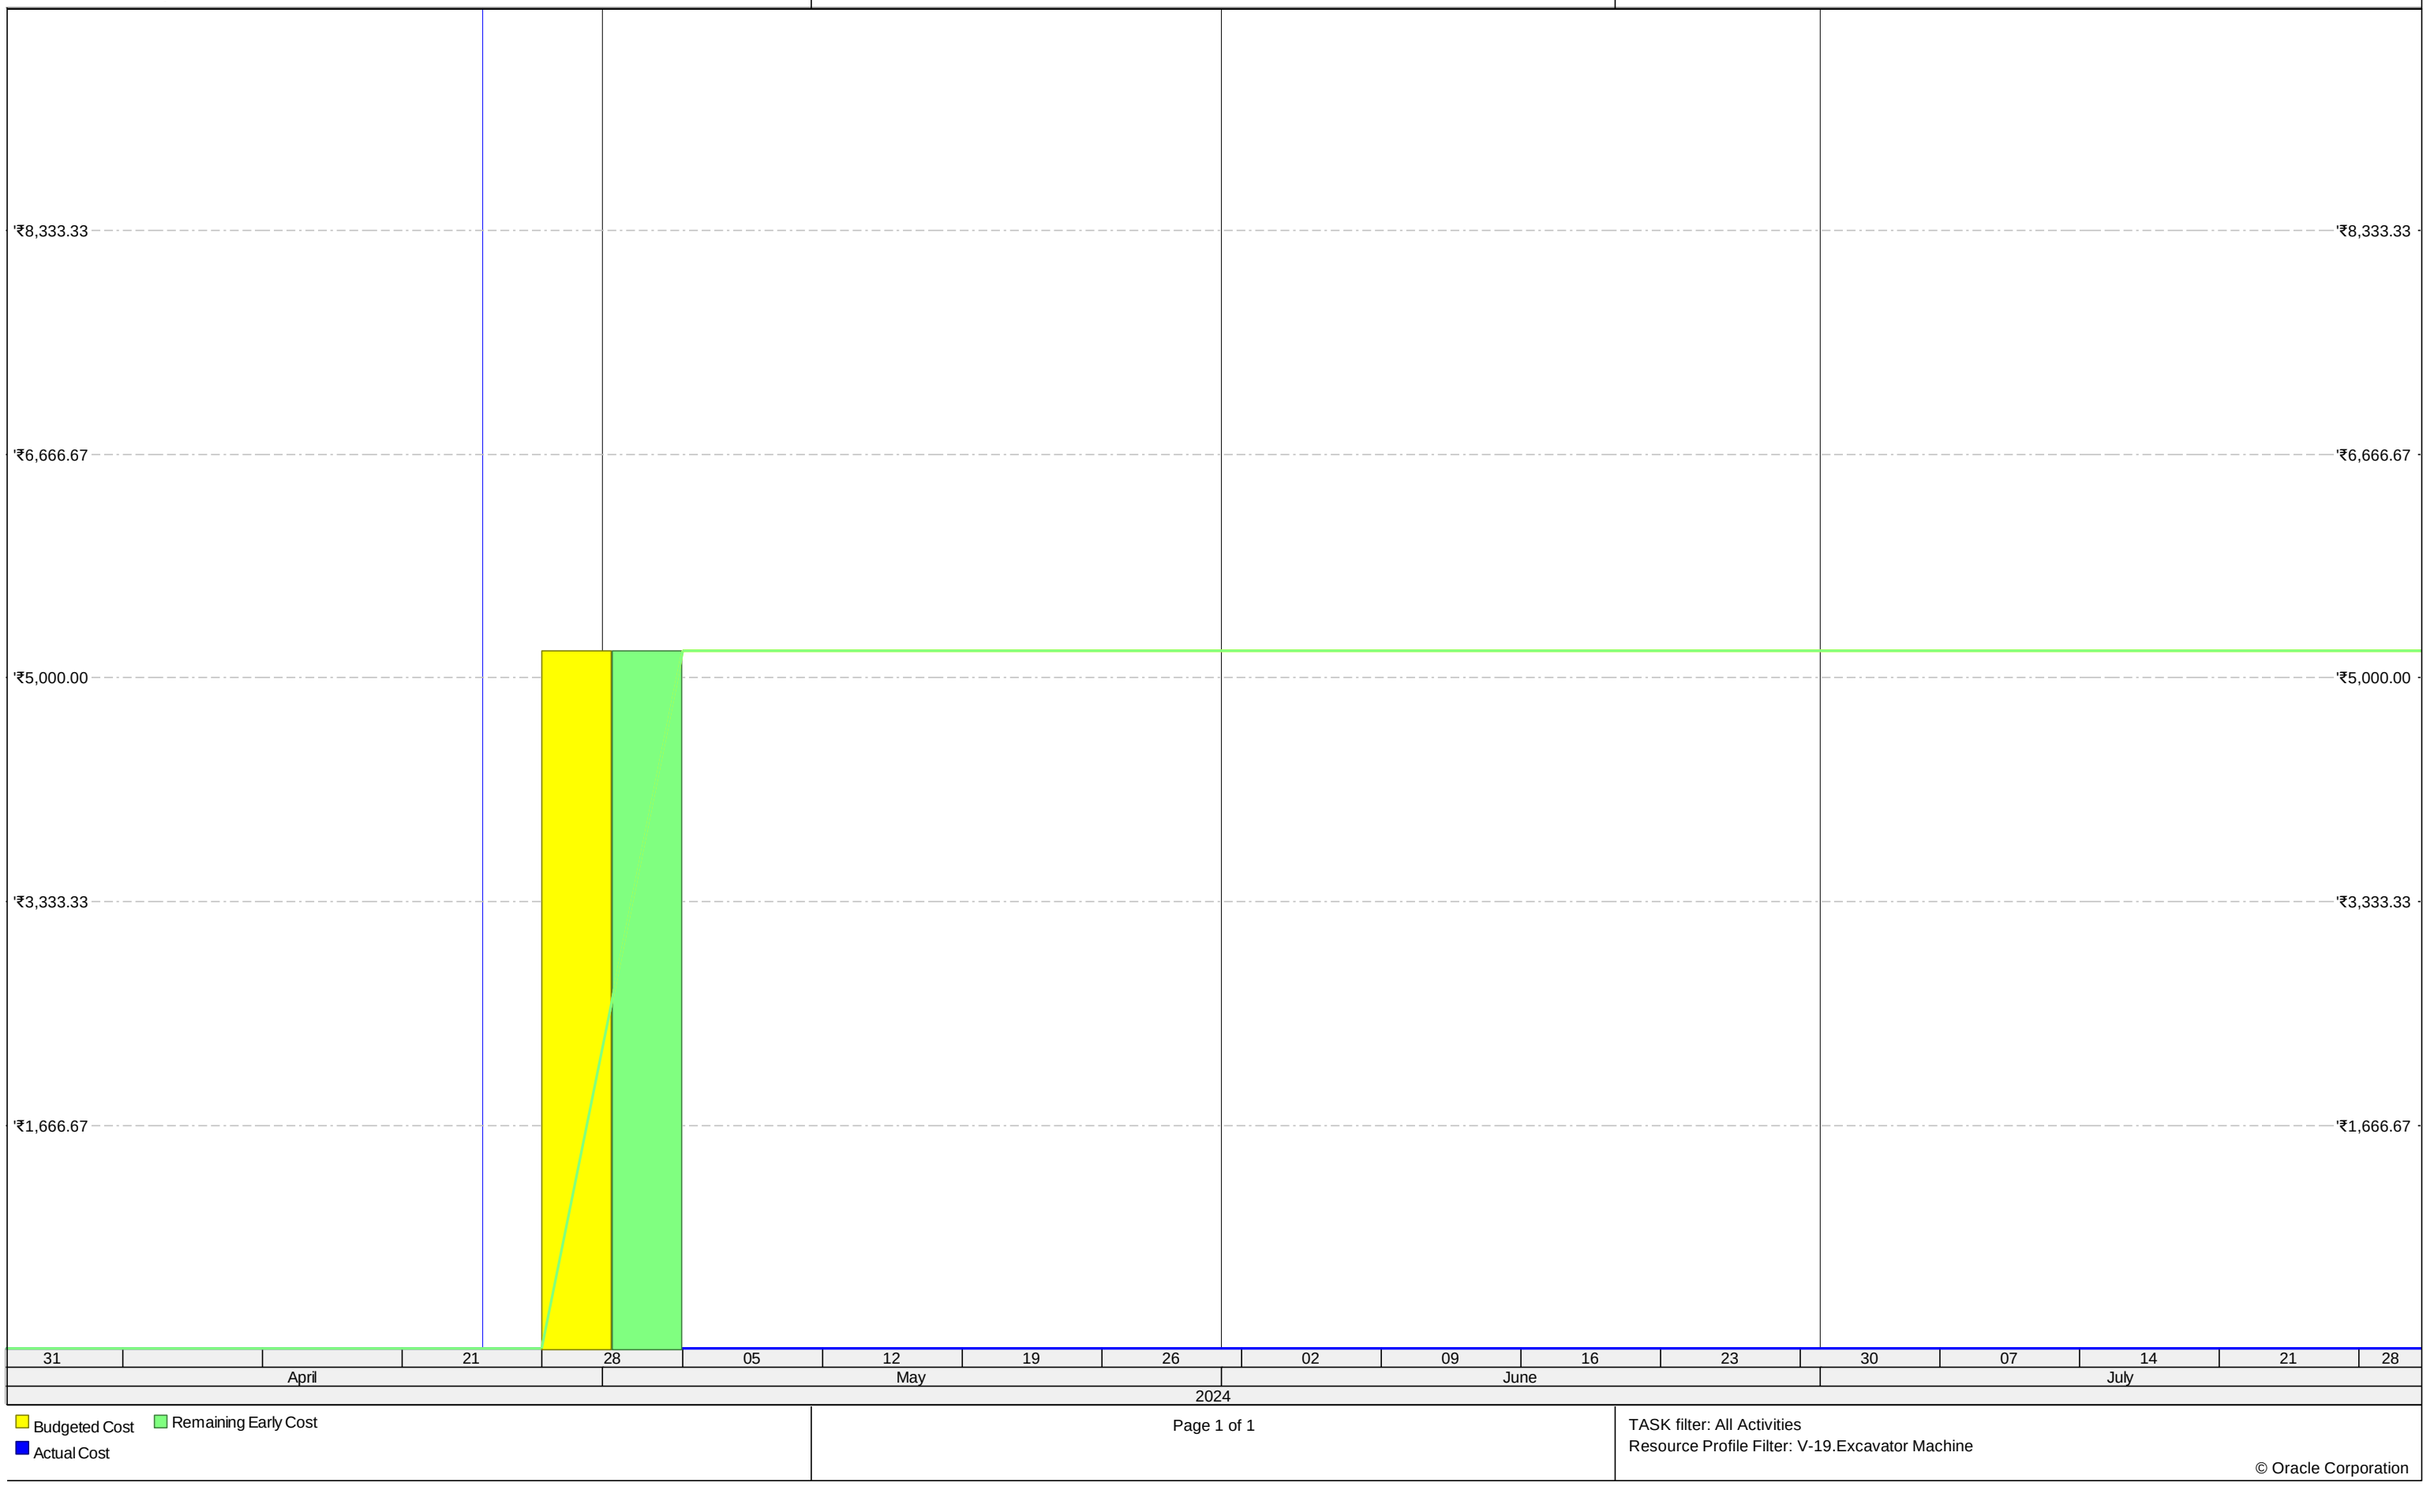

Budgeted Cost
Remaining Early Cost
Actual Cost

TASK filter: All Activities
Resource Profile Filter: V-19.Excavator Machine

© Oracle Corporation

REPORTS

RA-01 Resource Assignments, All Activities

User's Notes:

Resource Code / Project Code	Resource Name / WBS Code	Activity Code	Activity	Planned Units	Planned Duration	Planned Start	Planned Finish
V-1	**Mason**						
V-1000	V-1000.1	A1030	Foundation Masonary	152	3	03-May-24	08-May-24
V-1000	V-1000.1	A1030	Foundation Masonary	32	4	03-May-24	08-May-24
V-1000	V-1000.2.1	A1040	Pinth Beam	8	1	09-May-24	09-May-24
V-1000	V-1000.2.1	A1040	Pinth Beam	8	1	09-May-24	09-May-24
V-1000	V-1000.2.1	A1050	Block Work Masonary in Super Structure	168	7	10-May-24	20-May-24
V-1000	V-1000.2.1	A1080	Coloumn Concrete Work	8	1	22-May-24	22-May-24
V-1000	V-1000.2.1	A1110	Slab and Beam Concrete Work	16	1	05-Jun-24	05-Jun-24
V-1000	V-1000.2.2	A1120	Plaster Work	384	8	27-Jun-24	08-Jul-24
V-1000	V-1000.2.2	A1130	Flooring Work	16	1	09-Jul-24	09-Jul-24
			Total	**792**			
V-2	**Labourer**						
V-1000	V-1000.1	A1020	Excavation	80	1	02-May-24	02-May-24
V-1000	V-1000.1	A1020	Excavation	80	1	02-May-24	02-May-24
V-1000	V-1000.1	A1030	Foundation Masonary	240	4	03-May-24	08-May-24
V-1000	V-1000.1	A1030	Foundation Masonary	32	4	03-May-24	08-May-24
V-1000	V-1000.2.1	A1040	Pinth Beam	48	1	09-May-24	09-May-24
V-1000	V-1000.2.1	A1040	Pinth Beam	8	1	09-May-24	09-May-24
V-1000	V-1000.2.1	A1050	Block Work Masonary in Super Structure	100	3	10-May-24	15-May-24
V-1000	V-1000.2.1	A1080	Coloumn Concrete Work	48	1	22-May-24	22-May-24
V-1000	V-1000.2.1	A1110	Slab and Beam Concrete Work	96	1	05-Jun-24	05-Jun-24
V-1000	V-1000.2.2	A1120	Plaster Work	480	8	27-Jun-24	08-Jul-24
V-1000	V-1000.2.2	A1130	Flooring Work	96	1	09-Jul-24	09-Jul-24
			Total	**1308**			
V-3	**Carpenter**						
V-1000	V-1000.2.1	A1070	Coloumn Form Work	24	1	21-May-24	21-May-24
V-1000	V-1000.2.1	A1090	Slab And Beam form Work	144	6	23-May-24	30-May-24
			Total	**168**			
V-4	**Steel Welder**						
V-1000	V-1000.2.1	A1060	Coloum Steel Work	24	1	21-May-24	21-May-24
V-1000	V-1000.2.1	A1100	Slab and Beam Steel Work	72	3	31-May-24	04-Jun-24
			Total	**96**			
V-5	**Wood Worker**						
V-1000	V-1000.2.2	A1140	Window and Door Installation	80	1	10-Jul-24	10-Jul-24
			Total	**80**			

RA-01 Resource Assignments, All Activities

User's Notes:

Resource Code / Project Code	Resource Name / WBS Code	Activity Code	Activity	Planned Units	Planned Duration	Planned Start	Planned Finish
V-7	**Painter**						
V-1000	V-1000.2.2	A1150	Paint Work	208	4	11-Jul-24	17-Jul-24
			Total	**208**			
V-8	**Insecptor**						
V-1000	V-1000.3	A1160	Final Check List	8	1	17-Jul-24	18-Jul-24
			Total	**8**			
V-10	**Blocks**						
V-1000	V-1000.2.1	A1050	Block Work Masonary in Super Structure	56	7	10-May-24	20-May-24
			Total	**56**			
V-11	**Cement**	A1030	Foundation Masonary	32	4	03-May-24	08-May-24
V-1000	V-1000.1						
V-1000	V-1000.2.1	A1040	Pinth Beam	8	1	09-May-24	09-May-24
V-1000	V-1000.2.1	A1050	Block Work Masonary in Super Structure	56	7	10-May-24	20-May-24
V-1000	V-1000.2.1	A1080	Coloumn Concrete Work	8	1	22-May-24	22-May-24
V-1000	V-1000.2.1	A1110	Slab and Beam Concrete Work	8	1	05-Jun-24	05-Jun-24
V-1000	V-1000.2.2	A1120	Plaster Work	64	8	27-Jun-24	08-Jul-24
V-1000	V-1000.2.2	A1130	Flooring Work	8	1	09-Jul-24	09-Jul-24
			Total	**184**			
V-12	**Paint**						
V-1000	V-1000.2.2	A1150	Paint Work	35	4	11-Jul-24	17-Jul-24
			Total	**35**			
V-13	**Sand**						
V-1000	V-1000.1	A1030	Foundation Masonary	32	4	03-May-24	08-May-24
V-1000	V-1000.2.1	A1040	Pinth Beam	8	1	09-May-24	09-May-24
V-1000	V-1000.2.1	A1040	Pinth Beam	8	1	09-May-24	09-May-24
V-1000	V-1000.2.1	A1050	Block Work Masonary in Super Structure	56	7	10-May-24	20-May-24
V-1000	V-1000.2.1	A1080	Coloumn Concrete Work	8	1	22-May-24	22-May-24
V-1000	V-1000.2.1	A1110	Slab and Beam Concrete Work	8	1	05-Jun-24	05-Jun-24
V-1000	V-1000.2.2	A1120	Plaster Work	64	8	27-Jun-24	08-Jul-24
V-1000	V-1000.2.2	A1130	Flooring Work	8	1	09-Jul-24	09-Jul-24
			Total	**192**			
V-14	**Steel**						

RA-01 Resource Assignments, All Activities

User's Notes:

Resource Code	Resource Name	Project Code	WBS Code	Activity Code	Activity		Planned Units	Planned Duration	Planned Start	Planned Finish
		V-1000	V-1000.2.1	A1040	Pinth Beam		8	1	09-May-24	09-May-24
		V-1000	V-1000.2.1	A1060	Coloum Steel Work		8	1	21-May-24	21-May-24
		V-1000	V-1000.2.1	A1100	Slab and Beam Steel Work		24	3	31-May-24	04-Jun-24
						Total	**40**			
V-16	**Wood/Lintels**									
		V-1000	V-1000.2.1	A1070	Coloumn Form Work		8	1	21-May-24	21-May-24
		V-1000	V-1000.2.1	A1090	Slab And Beam form Work		48	6	23-May-24	30-May-24
						Total	**56**			
V-17	**Concrete Crushs**									
		V-1000	V-1000.2.1	A1080	Coloumn Concrete Work		8	1	22-May-24	22-May-24
		V-1000	V-1000.2.1	A1110	Slab and Beam Concrete Work		8	1	05-Jun-24	05-Jun-24
						Total	**16**			
V-18	**JCB**									
		V-1000	V-1000.0	A1010	Initial Prepatory Works		40	5	25-Apr-24	01-May-24
						Total	**40**			
V-19	**Excavator Machine**									
		V-1000	V-1000.1	A1020	Excavation		8	1	02-May-24	02-May-24
						Total	**8**			

RC-02 Resource Cost Control Report

User's Notes

Activity

Activity ID	Resource Name	Cost Account	Budgeted Cost	Units % Complete	Actual Cost	Remaining Early Cost	At Completion Cost
A1010	**Initial Prepatory Works**						
A1010	JCB		₹20,000.00	0%	₹0.00	₹20,000.00	₹20,000.00
Subtotal			**₹20,000.00**	**0%**	**₹0.00**	**₹20,000.00**	**₹20,000.00**
A1020	**Excavation**						
A1020	Excavator Machine		₹5,200.00	0%	₹0.00	₹5,200.00	₹5,200.00
A1020	Labourer		₹12,000.00	0%	₹0.00	₹12,000.00	₹12,000.00
A1020	Labourer		₹12,000.00	0%	₹0.00	₹12,000.00	₹12,000.00
Subtotal			**₹29,200.00**	**0%**	**₹0.00**	**₹29,200.00**	**₹29,200.00**
A1030	**Foundation Masonary**						
A1030	Sand		₹2,080.00	0%	₹0.00	₹2,080.00	₹2,080.00
A1030	Labourer		₹4,800.00	0%	₹0.00	₹4,800.00	₹4,800.00
A1030	Mason		₹6,400.00	0%	₹0.00	₹6,400.00	₹6,400.00
A1030	Cement		₹14,400.00	0%	₹0.00	₹14,400.00	₹14,400.00
A1030	Mason		₹30,400.00	0%	₹0.00	₹30,400.00	₹30,400.00
A1030	Labourer		₹36,000.00	0%	₹0.00	₹36,000.00	₹36,000.00
Subtotal			**₹94,080.00**	**0%**	**₹0.00**	**₹94,080.00**	**₹94,080.00**
A1040	**Pinth Beam**						
A1040	Sand		₹520.00	0%	₹0.00	₹520.00	₹520.00
A1040	Sand		₹520.00	0%	₹0.00	₹520.00	₹520.00
A1040	Steel		₹920.00	0%	₹0.00	₹920.00	₹920.00
A1040	Labourer		₹1,200.00	0%	₹0.00	₹1,200.00	₹1,200.00
A1040	Mason		₹1,600.00	0%	₹0.00	₹1,600.00	₹1,600.00
A1040	Mason		₹1,600.00	0%	₹0.00	₹1,600.00	₹1,600.00
A1040	Cement		₹3,600.00	0%	₹0.00	₹3,600.00	₹3,600.00
A1040	Labourer		₹7,200.00	0%	₹0.00	₹7,200.00	₹7,200.00
Subtotal			**₹17,160.00**	**0%**	**₹0.00**	**₹17,160.00**	**₹17,160.00**
A1050	**Block Work Masonary in Super Structure**						
A1050	Sand		₹3,640.00	0%	₹0.00	₹3,640.00	₹3,640.00
A1050	Blocks		₹8,400.00	0%	₹0.00	₹8,400.00	₹8,400.00
A1050	Labourer		₹15,000.00	0%	₹0.00	₹15,000.00	₹15,000.00
A1050	Cement		₹25,200.00	0%	₹0.00	₹25,200.00	₹25,200.00
A1050	Mason		₹33,600.00	0%	₹0.00	₹33,600.00	₹33,600.00
Subtotal			**₹85,840.00**	**0%**	**₹0.00**	**₹85,840.00**	**₹85,840.00**
A1060	**Coloum Steel Work**						
A1060	Steel		₹920.00	0%	₹0.00	₹920.00	₹920.00
A1060	Steel Welder		₹7,200.00	0%	₹0.00	₹7,200.00	₹7,200.00
Subtotal			**₹8,120.00**	**0%**	**₹0.00**	**₹8,120.00**	**₹8,120.00**
A1070	**Coloumn Form Work**						

RC-02 Resource Cost Control Report

User's Notes

Activity

Activity ID	Resource Name	Cost Account	Budgeted Cost	Units % Complete	Actual Cost	Remaining Early Cost	At Completion Cost
A1070	Carpenter		₹4,320.00	0%	₹0.00	₹4,320.00	₹4,320.00
A1070	Wood/Lintels		₹20,000.00	0%	₹0.00	₹20,000.00	₹20,000.00
Subtotal			**₹24,320.00**	**0%**	**₹0.00**	**₹24,320.00**	**₹24,320.00**
A1080	**Coloumn Concrete Work**						
A1080	Sand		₹520.00	0%	₹0.00	₹520.00	₹520.00
A1080	Mason		₹1,600.00	0%	₹0.00	₹1,600.00	₹1,600.00
A1080	Cement		₹3,600.00	0%	₹0.00	₹3,600.00	₹3,600.00
A1080	Labourer		₹7,200.00	0%	₹0.00	₹7,200.00	₹7,200.00
A1080	Concrete Crushs		₹53,600.00	0%	₹0.00	₹53,600.00	₹53,600.00
Subtotal			**₹66,520.00**	**0%**	**₹0.00**	**₹66,520.00**	**₹66,520.00**
A1090	**Slab And Beam form Work**						
A1090	Carpenter		₹25,920.00	0%	₹0.00	₹25,920.00	₹25,920.00
A1090	Wood/Lintels		₹120,000.00	0%	₹0.00	₹120,000.00	₹120,000.00
Subtotal			**₹145,920.00**	**0%**	**₹0.00**	**₹145,920.00**	**₹145,920.00**
A1100	**Slab and Beam Steel Work**						
A1100	Steel		₹2,760.00	0%	₹0.00	₹2,760.00	₹2,760.00
A1100	Steel Welder		₹21,600.00	0%	₹0.00	₹21,600.00	₹21,600.00
Subtotal			**₹24,360.00**	**0%**	**₹0.00**	**₹24,360.00**	**₹24,360.00**
A1110	**Slab and Beam Concrete Work**						
A1110	Sand		₹520.00	0%	₹0.00	₹520.00	₹520.00
A1110	Mason		₹3,200.00	0%	₹0.00	₹3,200.00	₹3,200.00
A1110	Cement		₹3,600.00	0%	₹0.00	₹3,600.00	₹3,600.00
A1110	Labourer		₹14,400.00	0%	₹0.00	₹14,400.00	₹14,400.00
A1110	Concrete Crushs		₹53,600.00	0%	₹0.00	₹53,600.00	₹53,600.00
Subtotal			**₹75,320.00**	**0%**	**₹0.00**	**₹75,320.00**	**₹75,320.00**
A1120	**Plaster Work**						
A1120	Sand		₹4,160.00	0%	₹0.00	₹4,160.00	₹4,160.00
A1120	Cement		₹28,800.00	0%	₹0.00	₹28,800.00	₹28,800.00
A1120	Labourer		₹72,000.00	0%	₹0.00	₹72,000.00	₹72,000.00
A1120	Mason		₹76,800.00	0%	₹0.00	₹76,800.00	₹76,800.00
Subtotal			**₹181,760.00**	**0%**	**₹0.00**	**₹181,760.00**	**₹181,760.00**
A1130	**Flooring Work**						
A1130	Sand		₹520.00	0%	₹0.00	₹520.00	₹520.00
A1130	Mason		₹3,200.00	0%	₹0.00	₹3,200.00	₹3,200.00
A1130	Cement		₹3,600.00	0%	₹0.00	₹3,600.00	₹3,600.00
A1130	Labourer		₹14,400.00	0%	₹0.00	₹14,400.00	₹14,400.00
Subtotal			**₹21,720.00**	**0%**	**₹0.00**	**₹21,720.00**	**₹21,720.00**

RC-02 Resource Cost Control Report

User's Notes

Activity

Activity ID	Resource Name	Cost Account	Budgeted Cost	Units % Complete	Actual Cost	Remaining Early Cost	At Completion Cost
A1140	**Window and Door Installation**						
A1140	Wood Worker		₹20,000.00	0%	₹0.00	₹20,000.00	₹20,000.00
Subtotal			**₹20,000.00**	**0%**	**₹0.00**	**₹20,000.00**	**₹20,000.00**
A1150	**Paint Work**						
A1150	Painter		₹31,200.00	0%	₹0.00	₹31,200.00	₹31,200.00
A1150	Paint		₹52,000.00	0%	₹0.00	₹52,000.00	₹52,000.00
Subtotal			**₹83,200.00**	**0%**	**₹0.00**	**₹83,200.00**	**₹83,200.00**
A1160	**Final Check List**						
A1160	Insecptor		₹9,600.00	0%	₹0.00	₹9,600.00	₹9,600.00
Subtotal			**₹9,600.00**	**0%**	**₹0.00**	**₹9,600.00**	**₹9,600.00**
Total			**₹907,120.00**	**0%**	**₹0.00**	**₹907,120.00**	**₹907,120.00**

Activity Relationships

WBS Activity Code	Predecessor	Activity ID	Successor	Activity ID	Relations Type
All Initiatives					
Residential Villa Project					
Priliminary Works					
A1010	Project Start	A1000	Initial Prepatory Works	A1010	FS
A1020	Initial Prepatory Works	A1010	Excavation	A1020	FS
Sub Structural Works					
A1030	Excavation	A1020	Foundation Masonary	A1030	FS
A1040	Foundation Masonary	A1030	Pinth Beam	A1040	FS
Super structional Works					
Structural Works		A1040	Block Work Masonary in Super Structure	A1050	FS
A1050	Pinth Beam				
A1060	Block Work Masonary in Super Structure	A1050	Coloum Steel Work	A1060	FS
A1070	Coloum Steel Work	A1060	Coloumn Form Work	A1070	FF
A1080	Coloumn Form Work	A1070	Coloumn Concrete Work	A1080	FS
A1090	Coloumn Concrete Work	A1080	Slab And Beam form Work	A1090	FS
A1100	Slab And Beam form Work	A1090	Slab and Beam Steel Work	A1100	FS
A1110	Slab and Beam Steel Work	A1100	Slab and Beam Concrete Work	A1110	FS
A1120	Slab and Beam Concrete Work	A1110	Plaster Work	A1120	FS
Architechtural works					
A1130	Plaster Work	A1120	Flooring Work	A1130	FS
A1140	Flooring Work	A1130	Window and Door Installation	A1140	FS
A1150	Window and Door Installation	A1140	Paint Work	A1150	FS
A1160	Paint Work	A1150	Final Check List	A1160	FS
Final Commisioning Work					
A1170	Final Check List	A1160	Project Handover	A1170	FS

© Oracle Corporation

Units of Measure

Unit Name	Abbreviati
Indian Rupee	₹
Number of Items	NOS
Cubic Feet	CFT
Square Feet	SQT
Kilograms	Kgs
Bags	BG
Tons	tons

© Oracle Corporation

END OF PROJECT
